

Mir Karam Ali Khan Talpur's Tomb Complex, Hyderabad




Center for Documentation and Conservation
of the Heritage of Sindh

Endowment Fund Trust for Preservation
of the Heritage of Sindh

CONSERVATION WORK



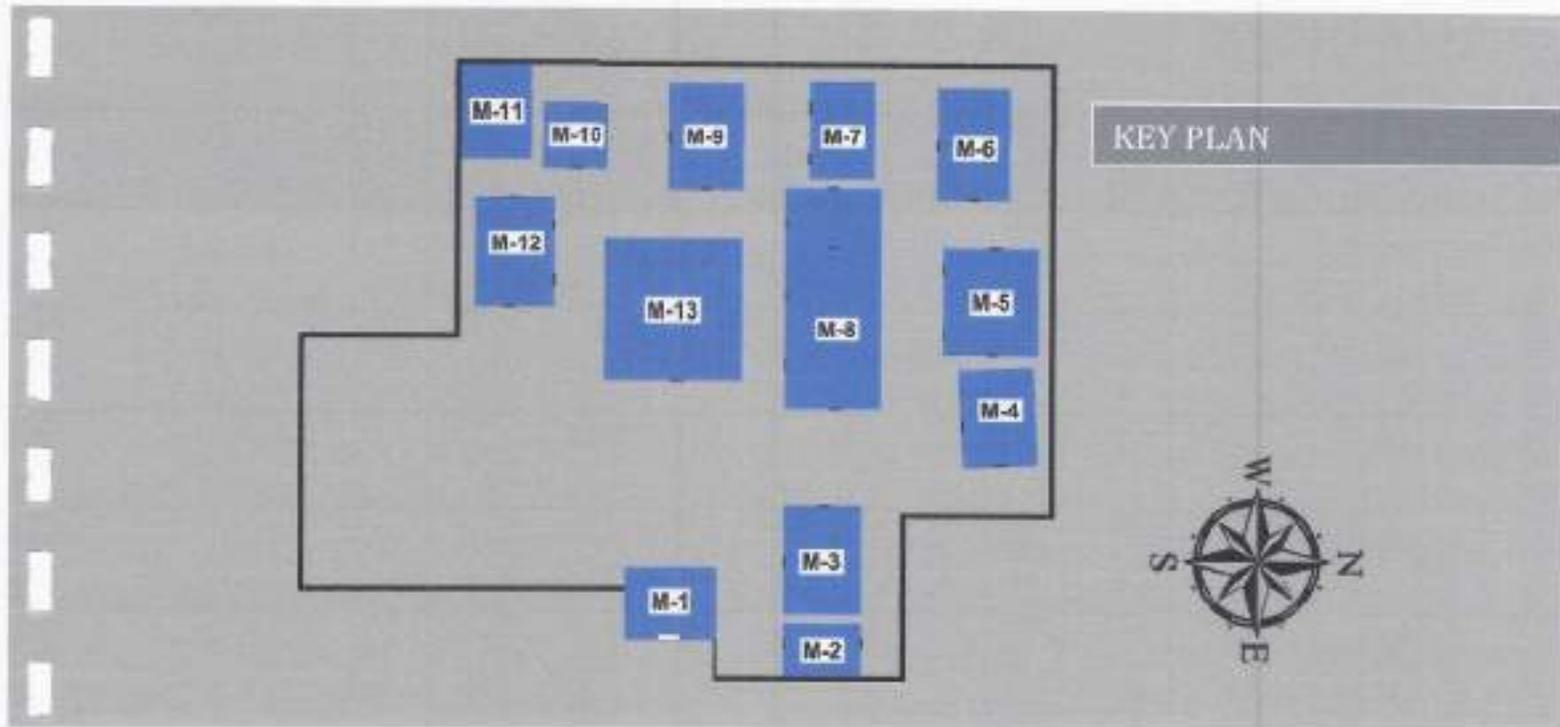

M-1 Entrance Gate

- Final plaster with lime and sandstone finishing of two panels of octagonal drum are completed.

M-3 Vaulted Roof Structure

- Final plaster with lime and sandstone finishing of vault is completed.
- Fixing of new kaashi tiles in five panels and fixing of old kaashi tiles in central panel of southern face are completed.

M-8 Flat Roof Structure

- Fixing of new kaashi tiles in two panels of eastern face is completed
- Fixing of old kaashi tiles in one panel of southern face is completed
- Fixing of base tiles is in final stage.

M-13 Mir Karam, Mi Khan Talpur Tomb

- New border tiles of drum are completely fixed.
- Fixing of new kaashi tiles in spandrel and border of one kiosk is completed
- First layer of lime plaster in arches of drum is completed.



M-1

M-3





M-8



M-8




M-13



CONSERVATION WORK PROGRESS

05

PROGRESS OF MIR KARAM ALI KHAN TALPUR
TOMB COMPLEX

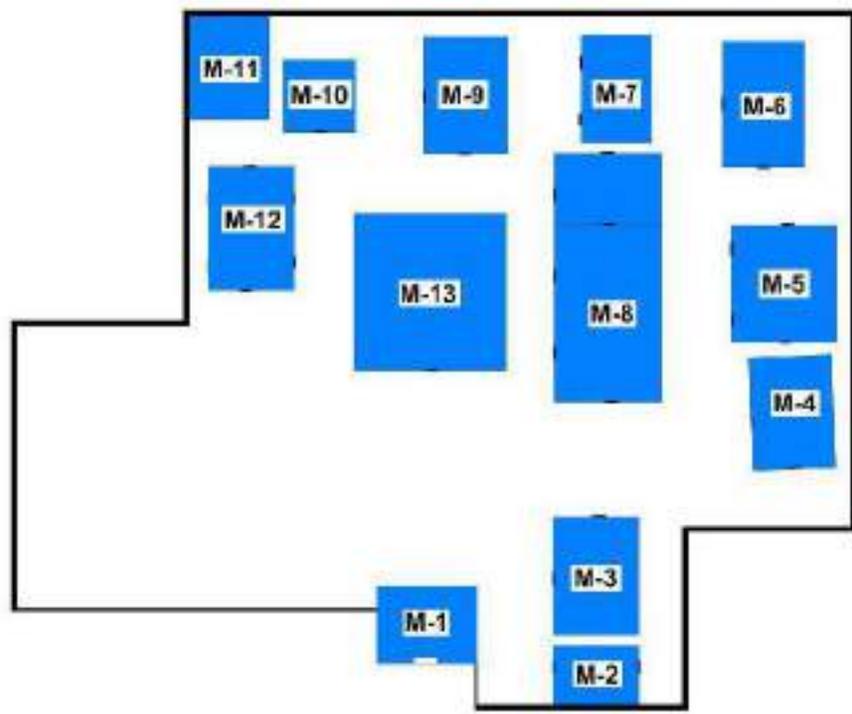

KEY PLAN

M13 - Mir Karam Ali Khan Talpur Tomb

- First layer of lime plaster on kiosks is fruitfully completed. (Page No.15)
- Lime plaster in facade is in practice. (Page No.14)
- Finials on kiosks have been fixed. (Page No.15)
- Kaashi tiles fixed in two remaining panels of facade. (Page No.15)
- Kaashi Tile (Jaali) is fixed in the central main arch. (Page No.15)

M1 - Entrance Gate

- Final lime plaster with soap stone finishing is completed in drum, its base and parapet walls is completed. (Page No.16)
- Kashi tiles in top border are fixed. (Page No.16)
- Lime plaster in western face is in process. (Page No.16)

M8 - Flat Roof Structure

- Fixing of kaashi tiles in arch above the door at eastern face is about to complete. (Page No.17)
- Fixing of tiles in dome of one kiosk is in process. (Page No.17)


M3 - Vaulted Roof Structure

- Fixing of kaashi tiles in two panels at western face is completed. (Page No.17)







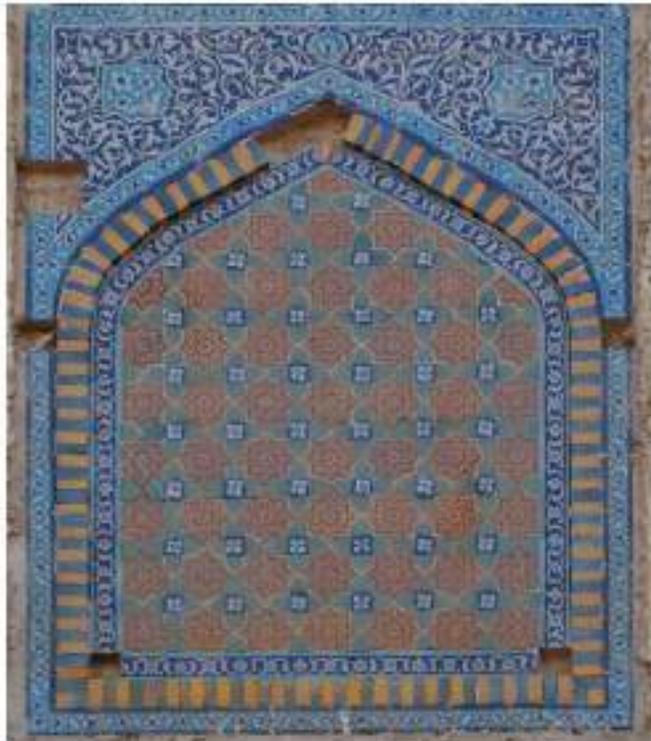

2

Conservation Progress**Mir Karam Ali Khan Talpur Tomb**

- Final lime plaster in facade of Mir Karam Ali Khan Talpur Tomb on borders of panels (Strips) is about 95% completed.
- Final Lime Plaster in kiosks of Mir Karam All Khan Talpur Tomb is ongoing and will be completed within a short span of time.
- Western side of entrance gate is furnished with final lime plaster (with soap stone finishing), about 85% percent is completed.
- Eastern side is finished with underpinning; the lime plaster work will be started soon.
- Border tile work is ongoing on Flat roofed structure in north of Mir Karam All Khan tomb.







Mir Karam Ali Khan Talpur Tomb

- Tile Work and lime plaster in facade of Mir Karam Ali Khan Talpur Tomb is about 97% completed.
- Final Lime Plaster in kiosks of Mir Karam Ali Khan Talpur Tomb is completed.
- Western side of entrance gate is furnished with final lime plaster (with soap stone finishing), about 95% percent is completed.
- On the eastern side of entrance gate lime plaster coating work is in progress.
- Border tile work at the top of Flat Roofed structure in north of Mir Karam Ali Khan Talpur Tomb is completed.
- Conservation of Turrets, Mir Naseer is under process which is in north of Mir Karam Ali Khan Tomb.
- Tile work at the top of wall and bottom of "Tajjar", North of Mir Naseer has been completed.





Mir Karam Ali Khan Talpur Tomb



Tile work at the top of wall and Bottom of "Tajjar" is completed



Tile work on the Turrets of Mir Naseer is under process which is in north of Mir Karam Ali Khan Talpur Tomb.



Mir Karam Ali Khan Talpur Tomb



On the eastern side of entrance gate lime coating and tile work is in progress



Border tile work is completed on Mir Karam Ali Khan Talpur tomb.



Mir Karam Ali Khan Talpur Tomb



Conservation of Turrets of Mir Naseer is under process which is in north of Mir Karam Ali Khan Talpur Tomb.

2 Conservation Progress

Mir Karam Ali Khan Talpur Tombs Complex

Mir Karam Ali Talpur`s Tomb:

- Tile Work & Lime Plaster in Facade of Mir Karam Ali Khan Talpur Tomb is About 98% Completed.
- Final Lime Plaster in kiosks of Mir Karam Ali Khan Talpur Tomb is completed, Three Finial are fixed on Kiosk of Mir Karam Ali Khan Talpur Tomb.
- Chirol, Lime Coating and Lime Plaster on the main arch of facade of Mir Karam Ali is completed.

Mir Naseer Talpur`s Tomb:

- Conservation of Turrets of Mir Naseer is completed which is in north of Mir Karam Ali Khan Talpur Tomb.

Tajjar


- Two rows tile work at the top of wall of "Tajjar" north of Mir Naseer has been completed.







2 Conservation Progress

Mir Karam Ali Khan Talpur Tombs Complex

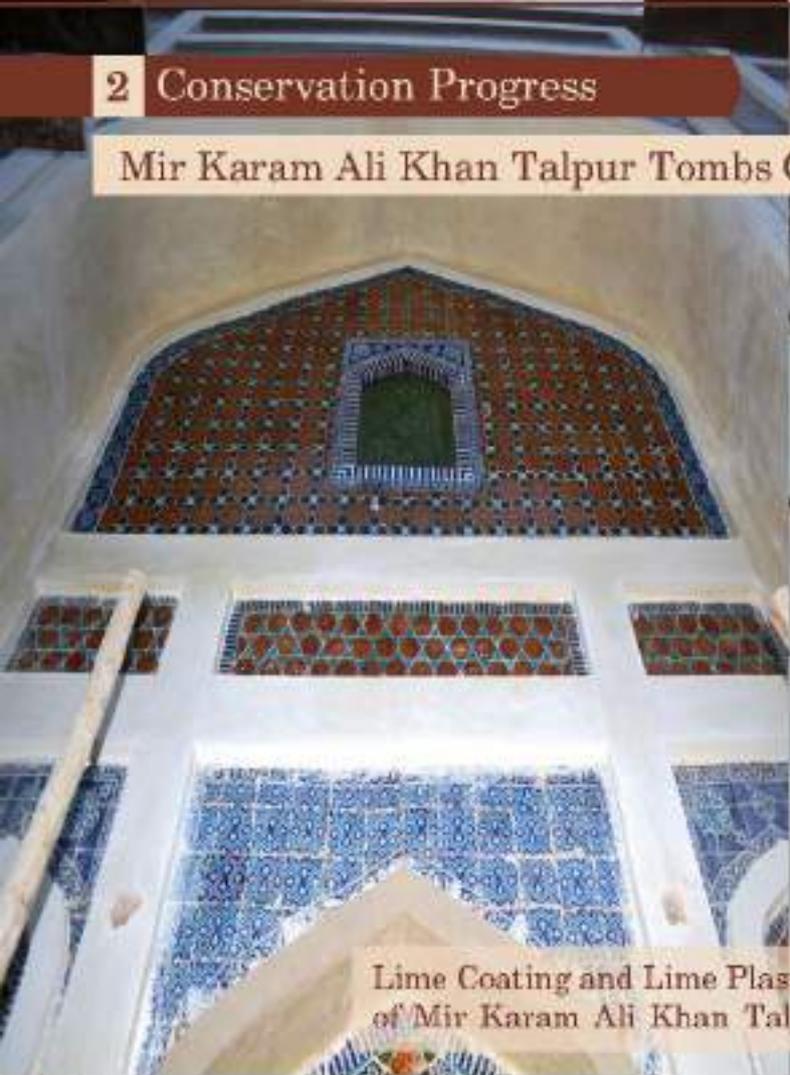


Lime Coating and Lime Plaster of Main Arch of Facade
of Mir Karam Ali Khan Talpur's Tomb is completed.

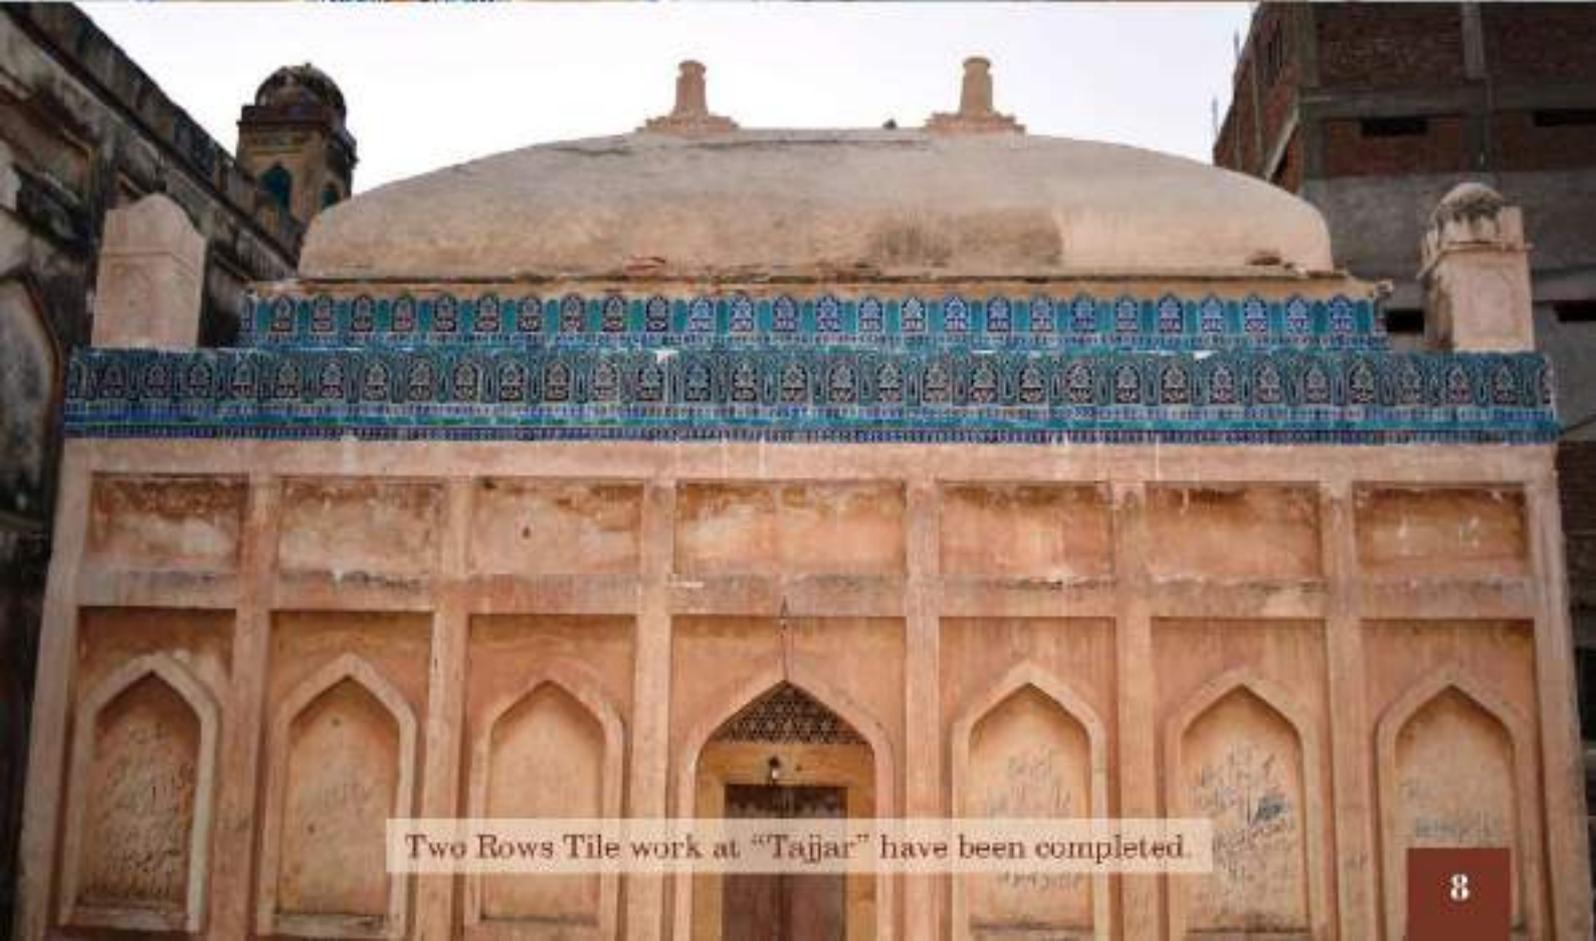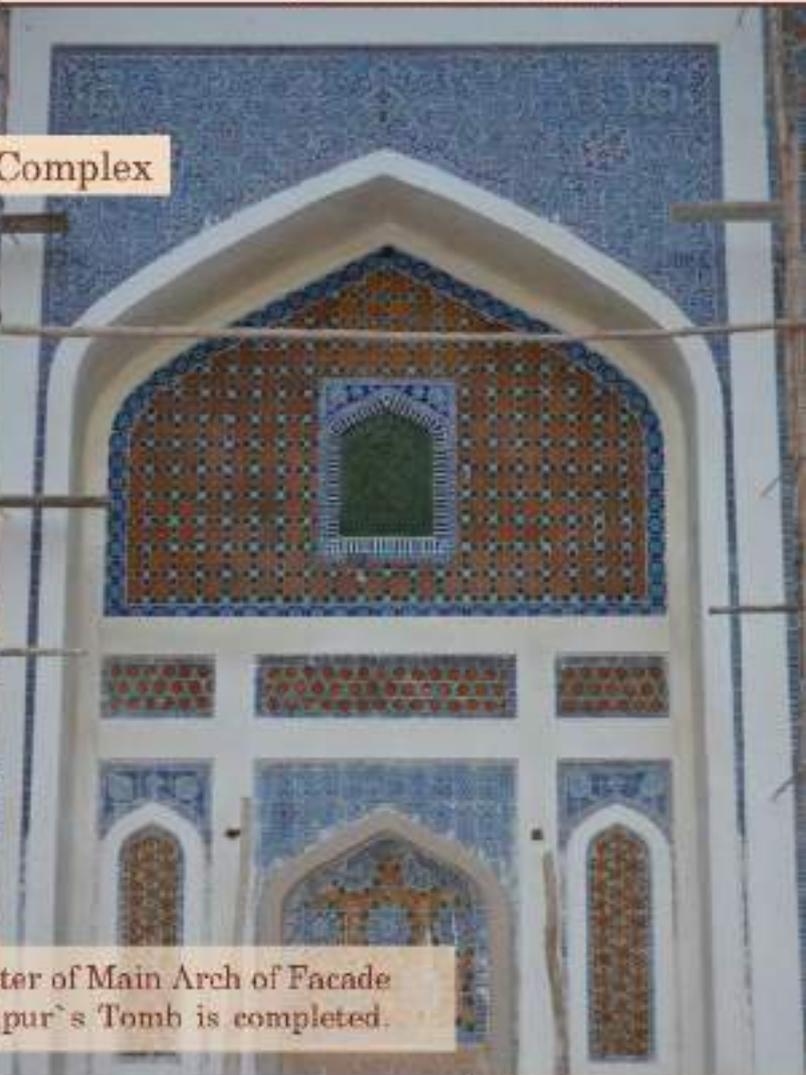


Two Rows Tile work at "Tajjar" have been completed.

2 Conservation Progress

Mir Karam Ali Khan Talpur Tombs Complex

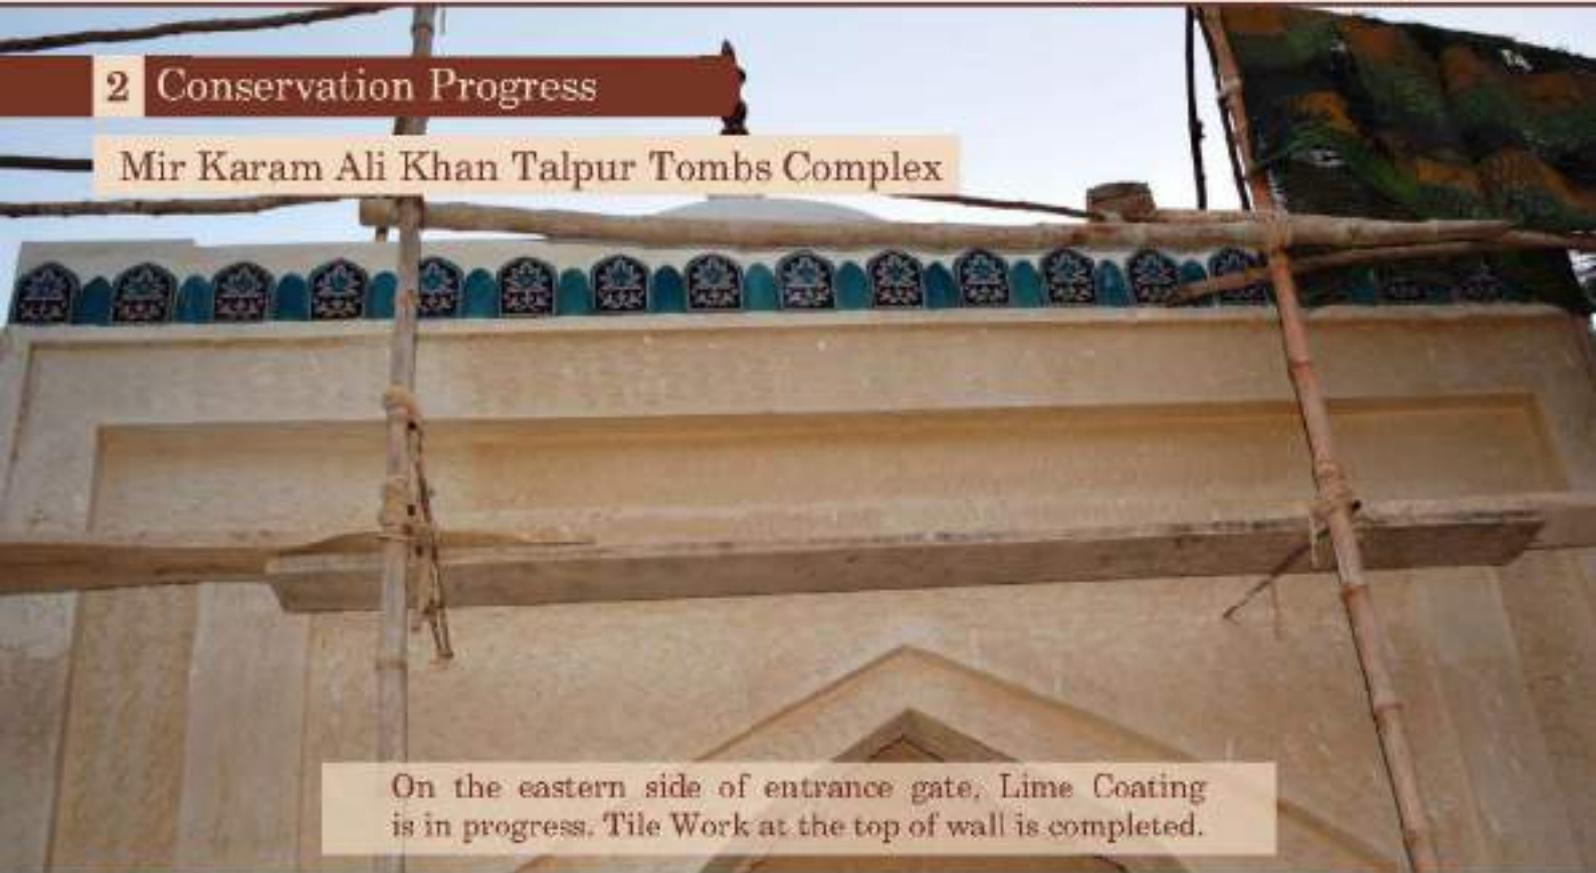

On the eastern side of entrance gate, Lime Coating is in progress. Tile Work at the top of wall is completed.

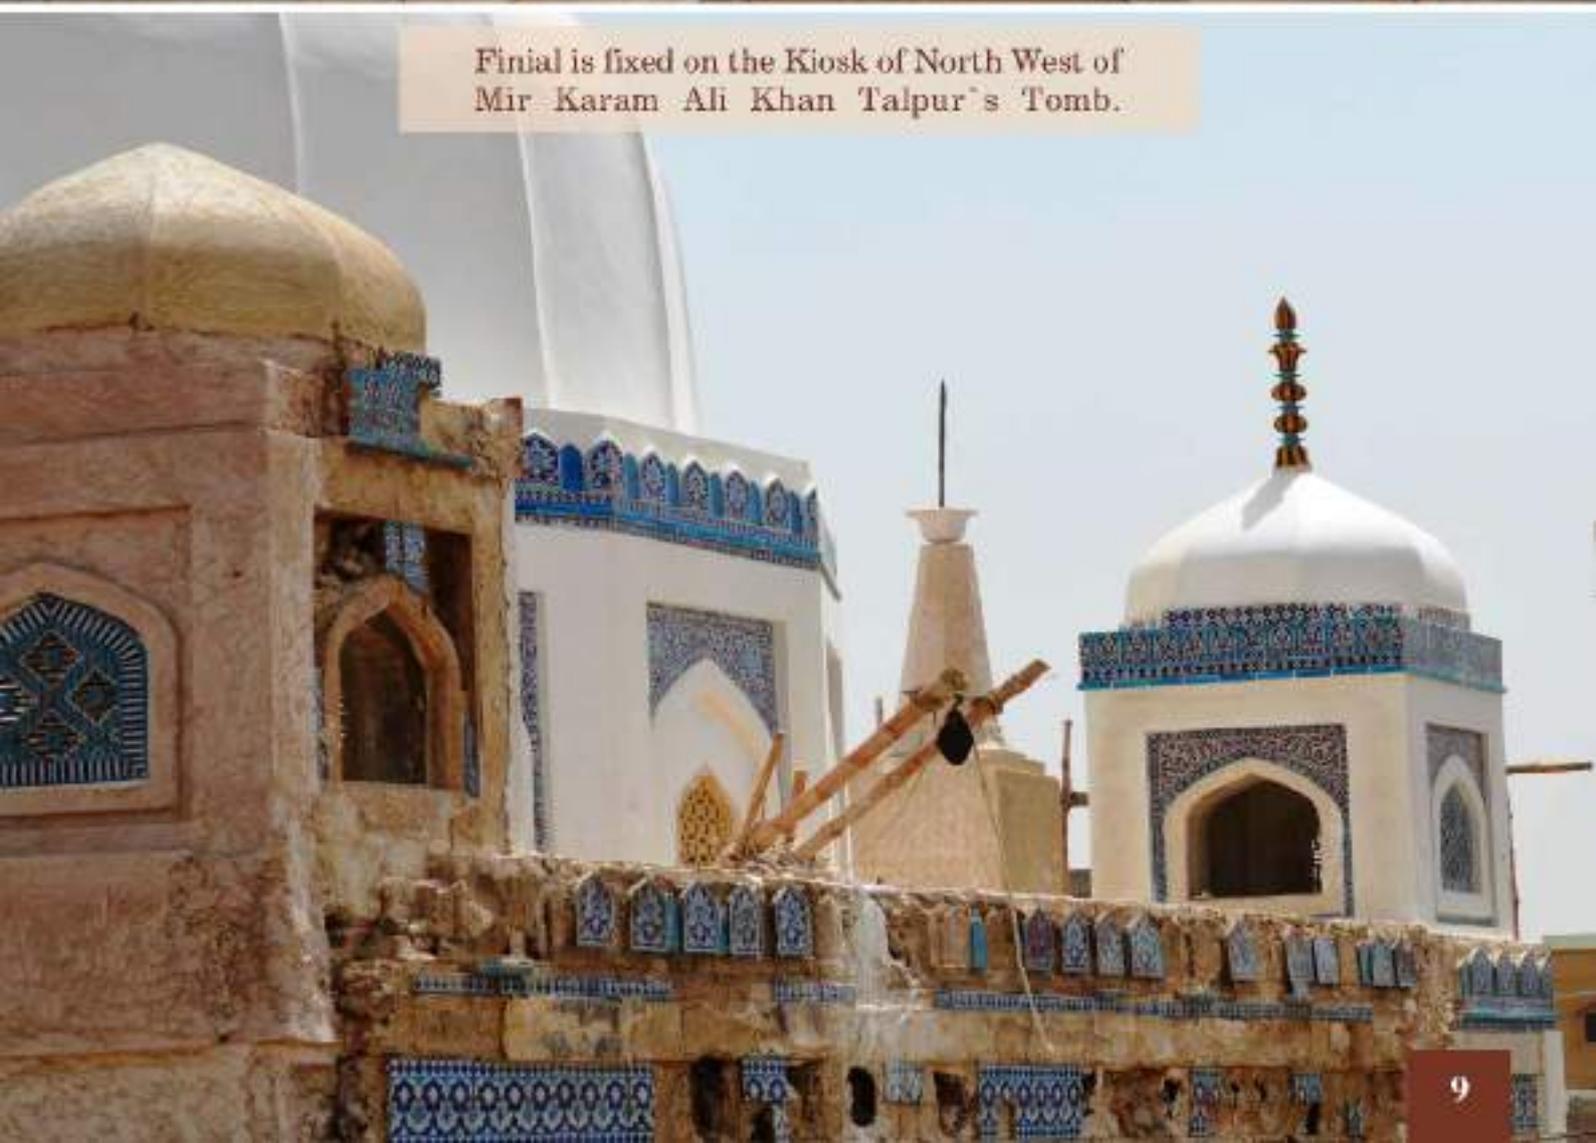

Finial is fixed on the Kiosk of North West of Mir Karam Ali Khan Talpur's Tomb.



CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tombs (Complex)

Mir Karam Ali Khan Talpur Tomb:

- Tile Work & Lime Plaster in Facade of Mir Karam Ali Khan Talpur Tomb is About 99% Completed.
- Final Lime Plaster in kiosks of Mir Karam Ali Khan Talpur Tomb is completed, Seven Finial are fixed on Kiosk of Mir Karam Ali Khan Talpur Tomb.
- Chirol, Lime Coating and Lime Plaster on the main arch of facade of Mir Karam Ali is completed.
- Turrents of Mir Karam Ali Khan Talpur are 98% Completed.
- Northern Side of Mir Karam Ali Khan Talpur is 30% Completed.
- Bottom & Top Arches of Northern Side of Mir Karam Ali Khan Talpur are completed.
- Top Borders (Musalah) of Northern side of Mir Karam Ali Khan Talpur are Completed.

Main Entrance:


- Eastern side of Main Entrance is 95% Completed.
- Western side of Main Entrance is also 95% Completed.

Mir Naseer Khan Talpur (Flat Roof Structure):

- Eastern side including Kiosks are 100% Completed.
- Southern side of Mir Naseer Khan Talpur is 60% Completed.

Tajjar:

- 80% Kashi Work is Completed of Tajjar wich is located in Nothern Side of Mir Naseer Khan Talpur.
- Chirol & Lime Coating of Kiosks of Tajjar is Completed.
- Lime Plaster work is in under process of Tajjar.
- Chirol & Lime Coating of Base of Finial is under process.

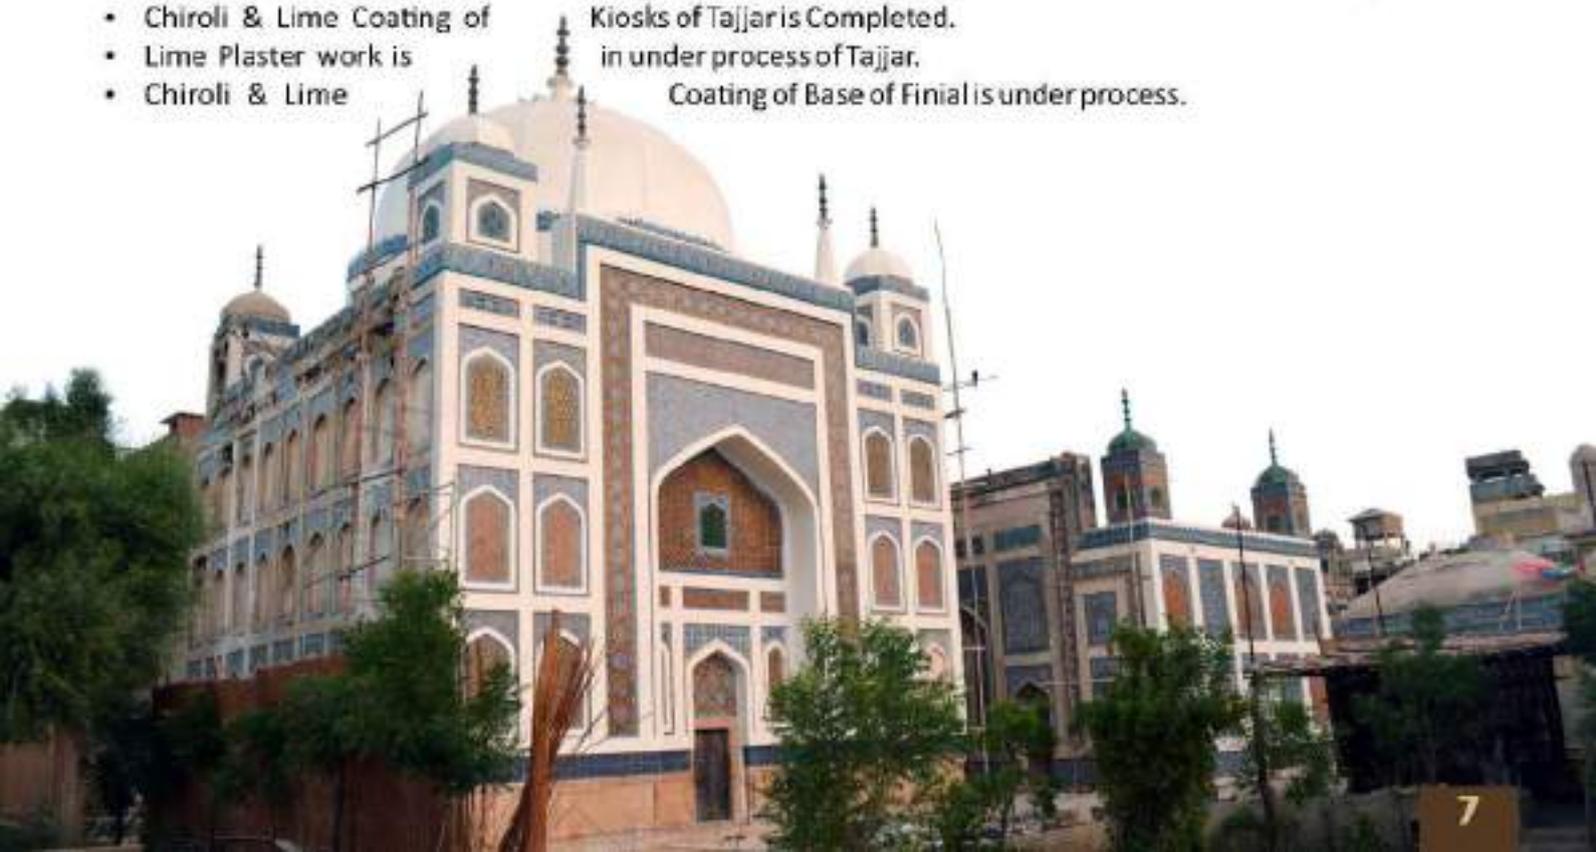



CONSERVATION PROGRESS

MIR KARAM ALI KHAN TALPUR TOMBS (COMPLEX)



Facade of Mir Karam Ali Khan Talpur Tomb



Finial of Mir Karam Ali Khan Talpur Tomb



Turrets (Tower) of Mir Karam Ali Khan Talpur Tomb



Kiosk of Northern & Western Side of Mir Karam Ali Khan Talpur Tomb



Northern Side of Mir Karam Ali Khan Talpur Tomb



CONSERVATION PROGRESS

MIR KARAM ALI KHAN TALPUR TOMBS (COMPLEX)



Western Side of Main Entrance Gate



Eastern Side Of Main Entrance Gate



Eastern Side of Mir Naseer Khan Talpur



Southern & Eastern Side of
Mir Naseer Khan Talpur



Southern & Eastern Side of Tajar




Top View of Tajar




Conservation Progress

Mir Karam Ali Khan Talpur Tombs Complex

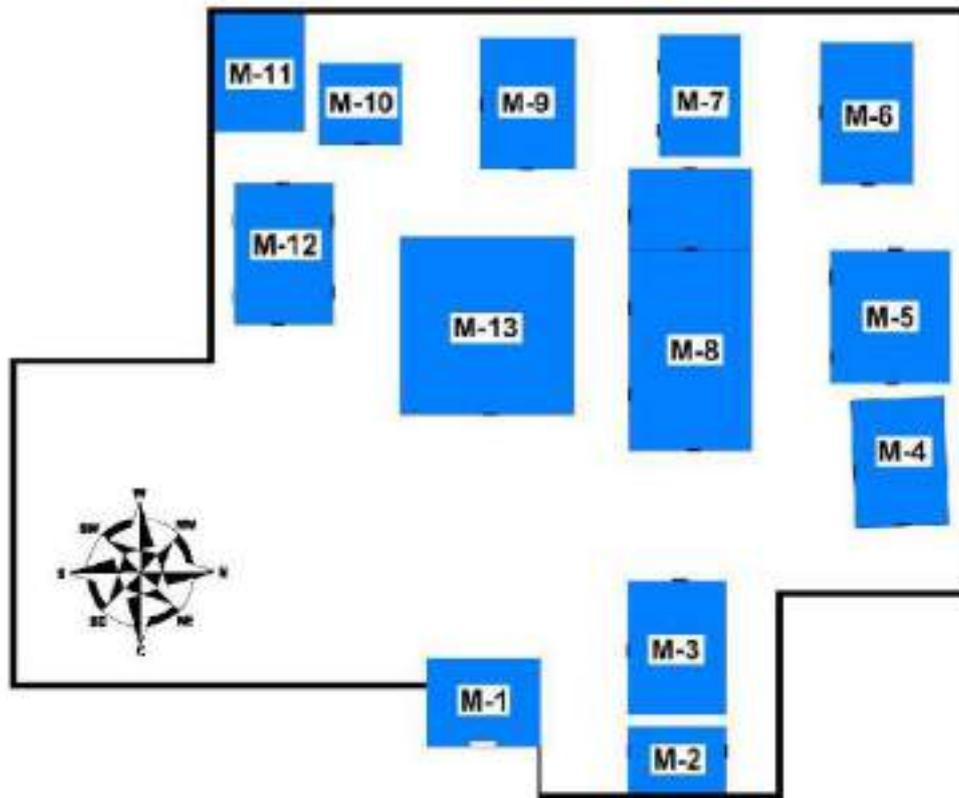

KEY PLAN





Conservation Progress

Mir Karam Ali Khan Talpur Tombs Complex

M-13 | Mir Karam Ali Khan Talpur Tomb

- Tile Work & Lime Plaster in Facade of Mir Karam Ali Khan Talpur Tomb is About 99% Completed.
- Final Lime Plaster in kiosks of Mir Karam Ali Khan Talpur Tomb is completed, Seven Finial are fixed on Kiosk of Mir Karam Ali Khan Talpur Tomb.
- Chiroli, Lime Coating and Lime Plaster on the main arch of facade of Mir Karam Ali is completed.
- Turrents of Mir Karam Ali Khan Talpur are 98% Completed.
- Northern Side of Mir Karam Ali Khan Talpur is 60% Completed.
- Bottom & Top Arches of Northern Side of Mir Karam Ali Khan Talpur are completed.
- Top Borders (Musalah) of Northern side of Mir Karam Ali Khan Talpur are Completed.
- Final Lime Plaster of two top horizontal Lime Borders at the top of northern side of tomb is completed.
- Seven Arches of Original kashi tiles at northern side of tomb are re-fixed.
- Kashi tiles beside top border (Musallah) on the northern side of Mir Karam Ali Khan Tomb are fixed.
- Old Kashi Tiles at the bottom (Izhoro) on the northern side of Mir Karam Ali Khan Talpur Tomb is re-fixed.

M-1 | Entrance Gate

- Eastern side of Main Entrance is 95% Completed.
- Western side of Main Entrance is also 95% Completed.
-

M-8 | Flat Roof Structure


- Eastern side including Kiosks are 100% Completed.
- Kashi (Musalah) has been placed at the top of monument.
- Lime Plaster at the Borders at facade of monument is completed.
- Southern side of Mir Naseer Khan Talpur is 60% Completed.

M-4 | Vaulted Roof Structure

- 80% Kashi Work is Completed of Tajjar wich is located in Northern Side of Mir Naseer Khan Talpur.
- Chiroli & Lime Coating of Kiosks of Tajjar is Completed.
- Lime Plaster at the top of vaulted roof is under process.
- Chiroli & Lime Coating of Base of Finial is under process.
- Two Finial at the top of vaulted roof are restored.

M-3 | Vaulted Roof Structure

- Fixing of Kashi Tiles at west side of "Tajjar" at north east side of Mir Karam Ali Tomb is Completed.



Conservation Progress

Mir Karam Ali Khan Talpur Tombs Complex



Facade of Mir Karam Ali Khan Talpur Tomb



Conservation Progress

Mir Karam Ali Khan Talpur Tombs Complex




Northern Side of Mir Karam Ali Khan Talpur Tomb



Conservation Progress

Mir Karam Ali Khan Talpur Tombs Complex

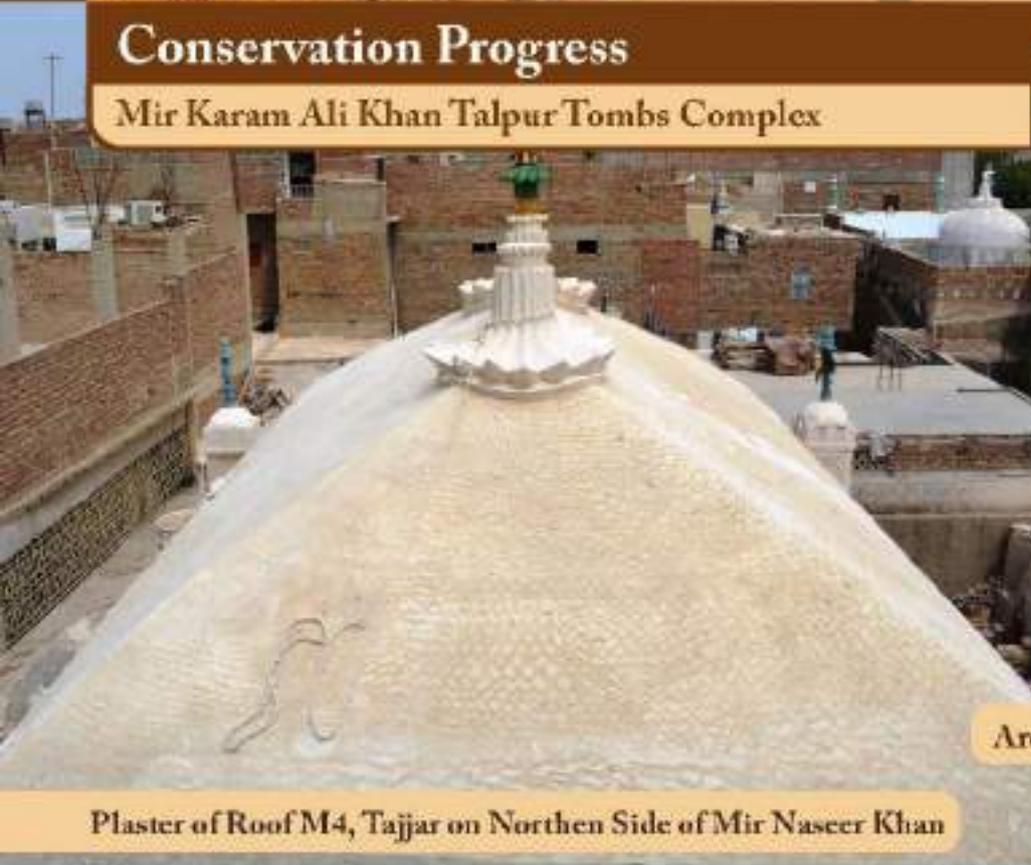

Plaster of Roof M4, Tajar on Northern Side of Mir Naseer Khan



Arch of Mir Karam Ali Khan Talpur Tomb




Northern Side of Mir Karam Ali Khan Talpur Tomb




Conservation Progress

Mir Karam Ali Khan Talpur Tombs Complex

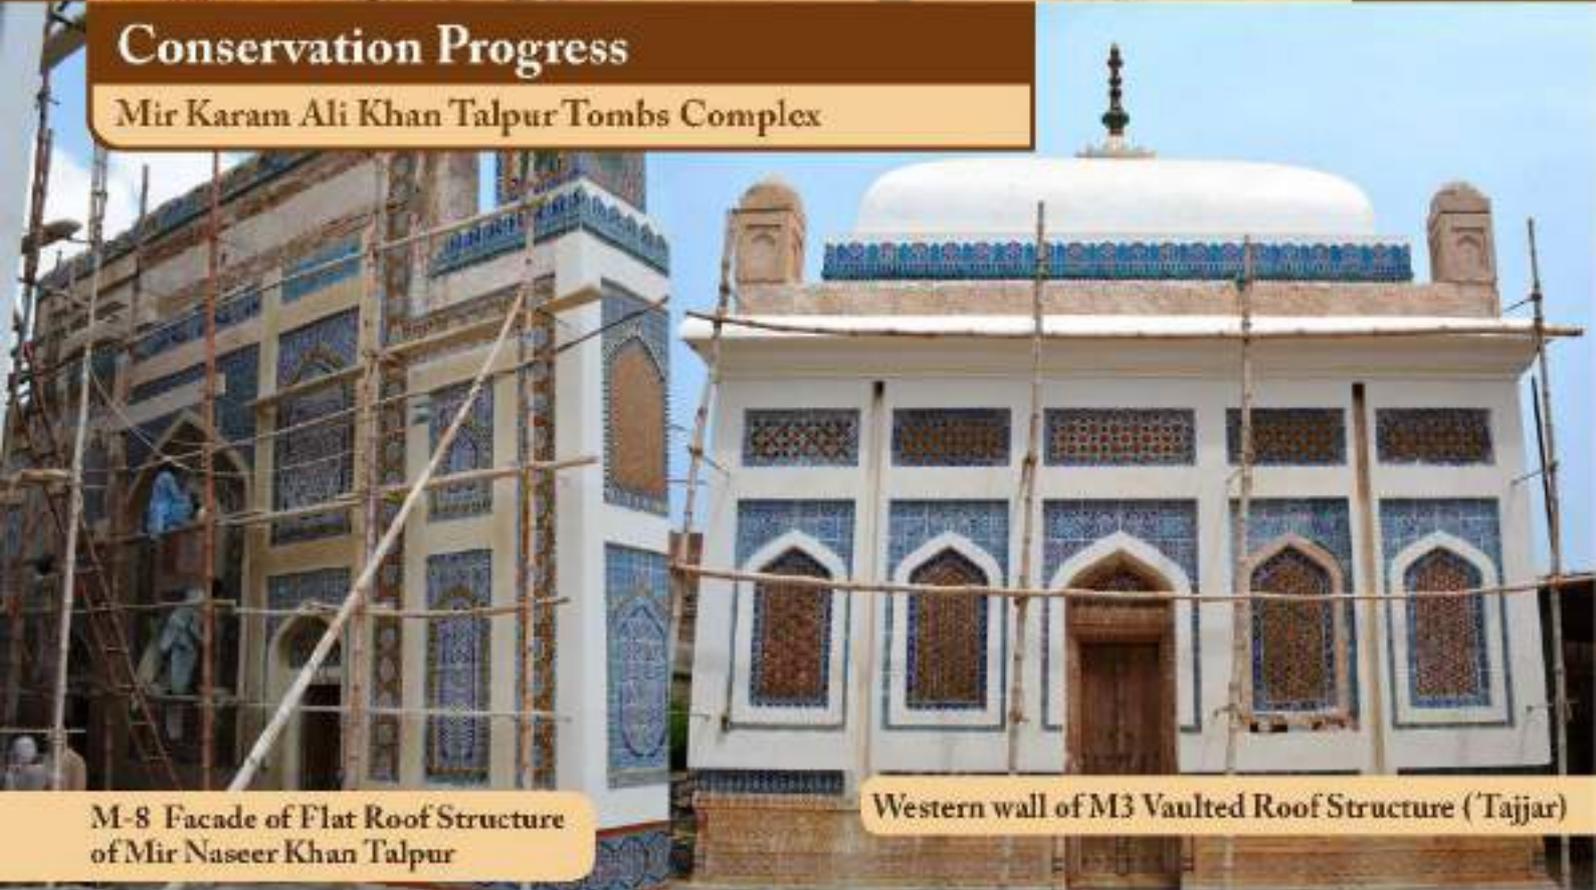

M-8 Facade of Flat Roof Structure of Mir Naseer Khan Talpur


Western wall of M3 Vaulted Roof Structure ('Tajjar)

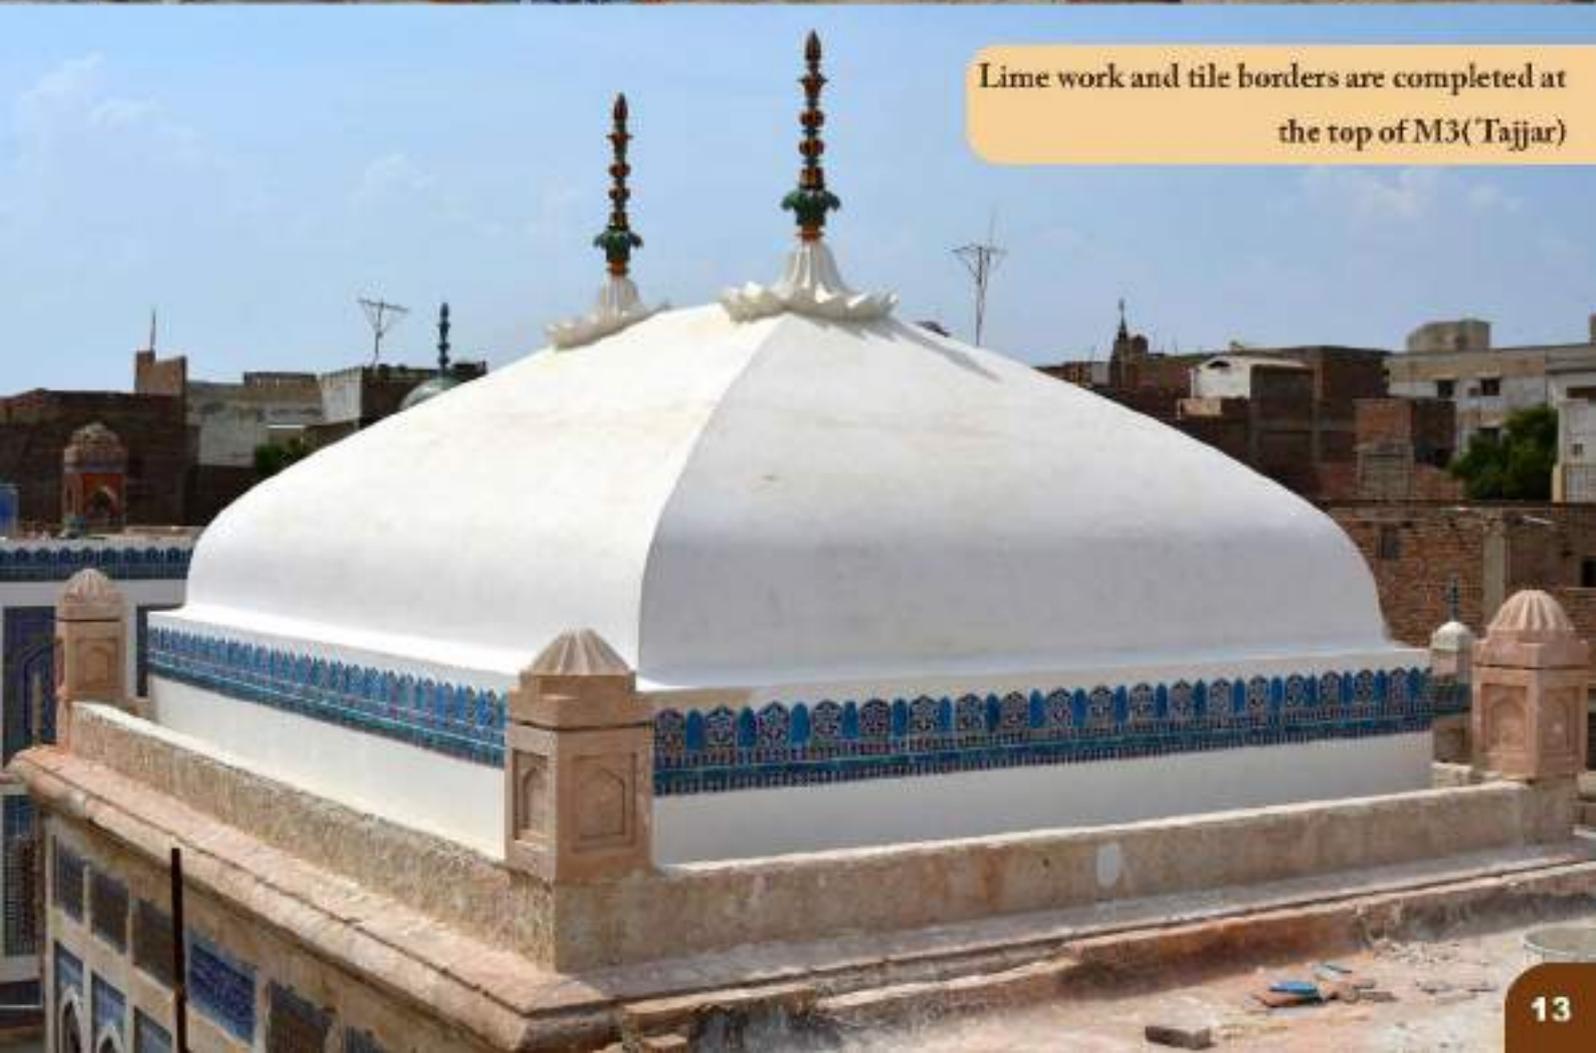

Lime work and tile borders are completed at the top of M3('Tajjar)

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tomb's Complex

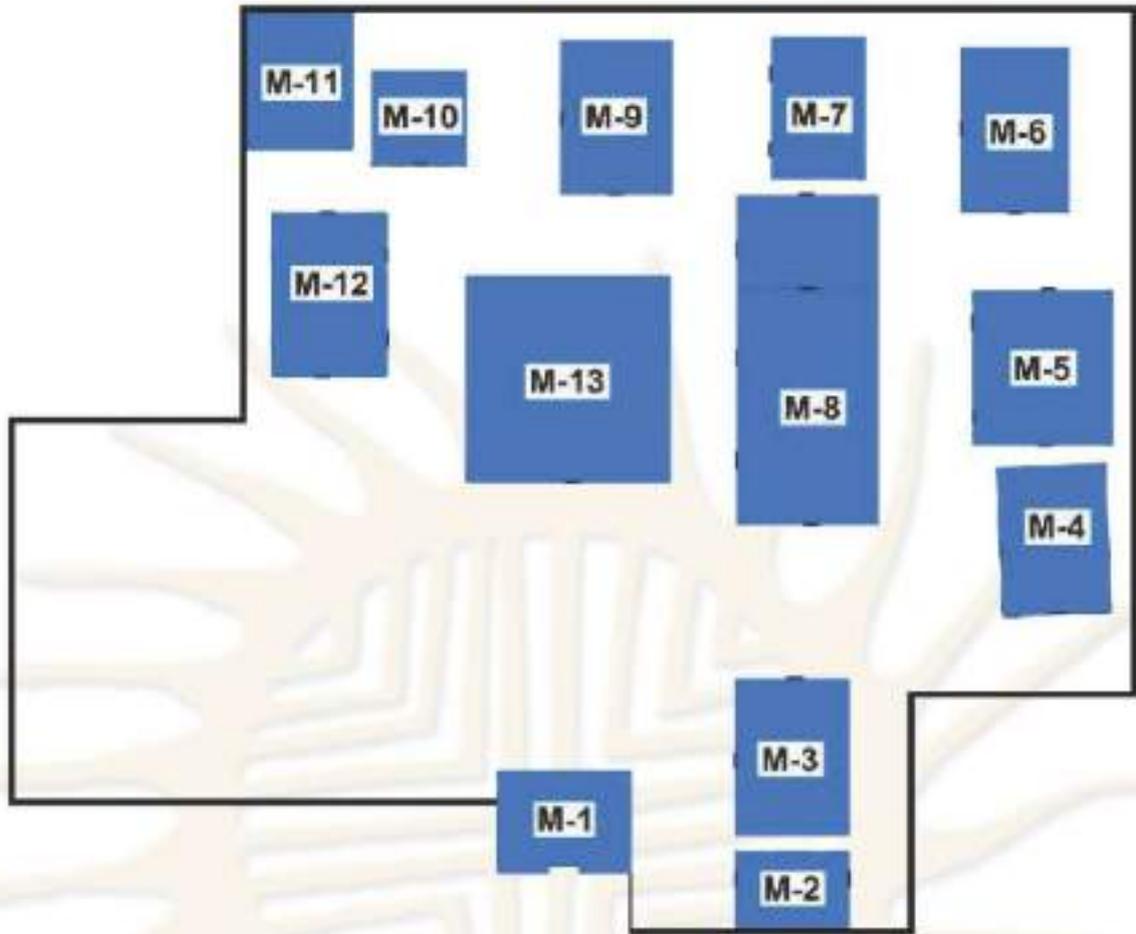

KEY PLAN



M-13 | Mir Karam Ali Khan Talpur Tomb

- Tile Work & Lime Plaster in Facade of Mir Karam Ali Khan Talpur Tomb is about 99% Completed.
- Final Lime Plaster in kiosks of Mir Karam Ali Khan Talpur Tomb is completed, Seven Finial are fixed on Kiosk of Mir Karam Ali Khan Talpur Tomb.
- Chiroll, Lime Coating and Lime Plaster on the main arch of facade of Mir Karam Ali is completed.
- Turrents of Mir Karam Ali Khan Talpur are 98% Completed.
- Northern Side of Mir Karam Ali Khan Talpur is 100% Completed.
- Bottom & Top Arches of Northern Side of Mir Karam Ali Khan Talpur are completed.
- Top Borders (Musalah) of Northern side of Mir Karam Ali Khan Talpur are completed.
- Final Lime Plaster of two top horizontal Lime Borders at the top of northern side of tomb is completed.
- Seven Arches of Original kashi tiles at northern side of tomb are re-fixed.
- Kashi tiles beside top border (Musallah) on the northern side of Mir Karam Ali Khan Tomb are fixed.
- Old Kashi Tiles at the bottom (Izhoro) on the northern side of Mir Karam Ali Khan Talpur Tomb is re-fixed.
- Kasha tiles on the top border of southern side is restored.
- Kashi in two top arches on the southern side are completed.

M-1 | Entrance Gate

- Eastern side of Main Entrance is 95% Completed.
- Western side of Main Entrance is also 95% Completed.

M-8 | Flat Roof Structure

- Eastern side including Kiosks are 100% Completed.
- Kashi (Musalah) has been placed at the top of monument.
- Lime Plaster at the Borders at facade of monument is completed.
- Southern side of Mir Naseer Khan Talpur is 70% Completed.
- Kasha tiles on the horizontal pands on the top of structure are restored.

M-4 | Vaulted Roof Structure

- 80% Kashi Work is Completed of Tajjar which is located in Northern Side of Mir Naseer Khan Talpur.
- Chiroll & Lime Coating of Kiosks of Tajjar is completed.
- Lime Plaster at the top of vaulted roof is completed.
- Chiroll & Lime Coating of Base of Finial is completed.
- Two Finial at the top of vaulted roof are restored.
- Tile is fixed on façade and lime work is in progress.

M-3 | Vaulted Roof Structure

- Fixing of Kashi Tiles at west side of "Tajjar" at north east side of Mir Karam Ali Tomb is completed.
- Lime plaster at the top of vaulted roof is completed.
- Fixing of kashi on the northern side of Tajjar is in progress.

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tomb's Complex

ENDOWMENT FUND TRUST | For the Preservation of the Heritage of Sindh



CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tomb's Complex

ENDOWMENT FUND TRUST | For the Preservation of the Heritage of Sindh



Northern side of Mir Karam Ali Tomb Talpur is Completed

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tomb's Complex

ENDOWMENT FUND TRUST | For the Preservation of the Heritage of Sindh



Kiosk of Western Side of Mir Karam Ali Tomb

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tomb's Complex

ENDOWMENT FUND TRUST | For the Preservation of the Heritage of Sindh




Tiles are fixed on southern side on the top border of Mir Karam Ali Talpur Tomb



Tiles are Fixed at the Facade of Top Border of Mir Nasir Tomb

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tomb`s Complex

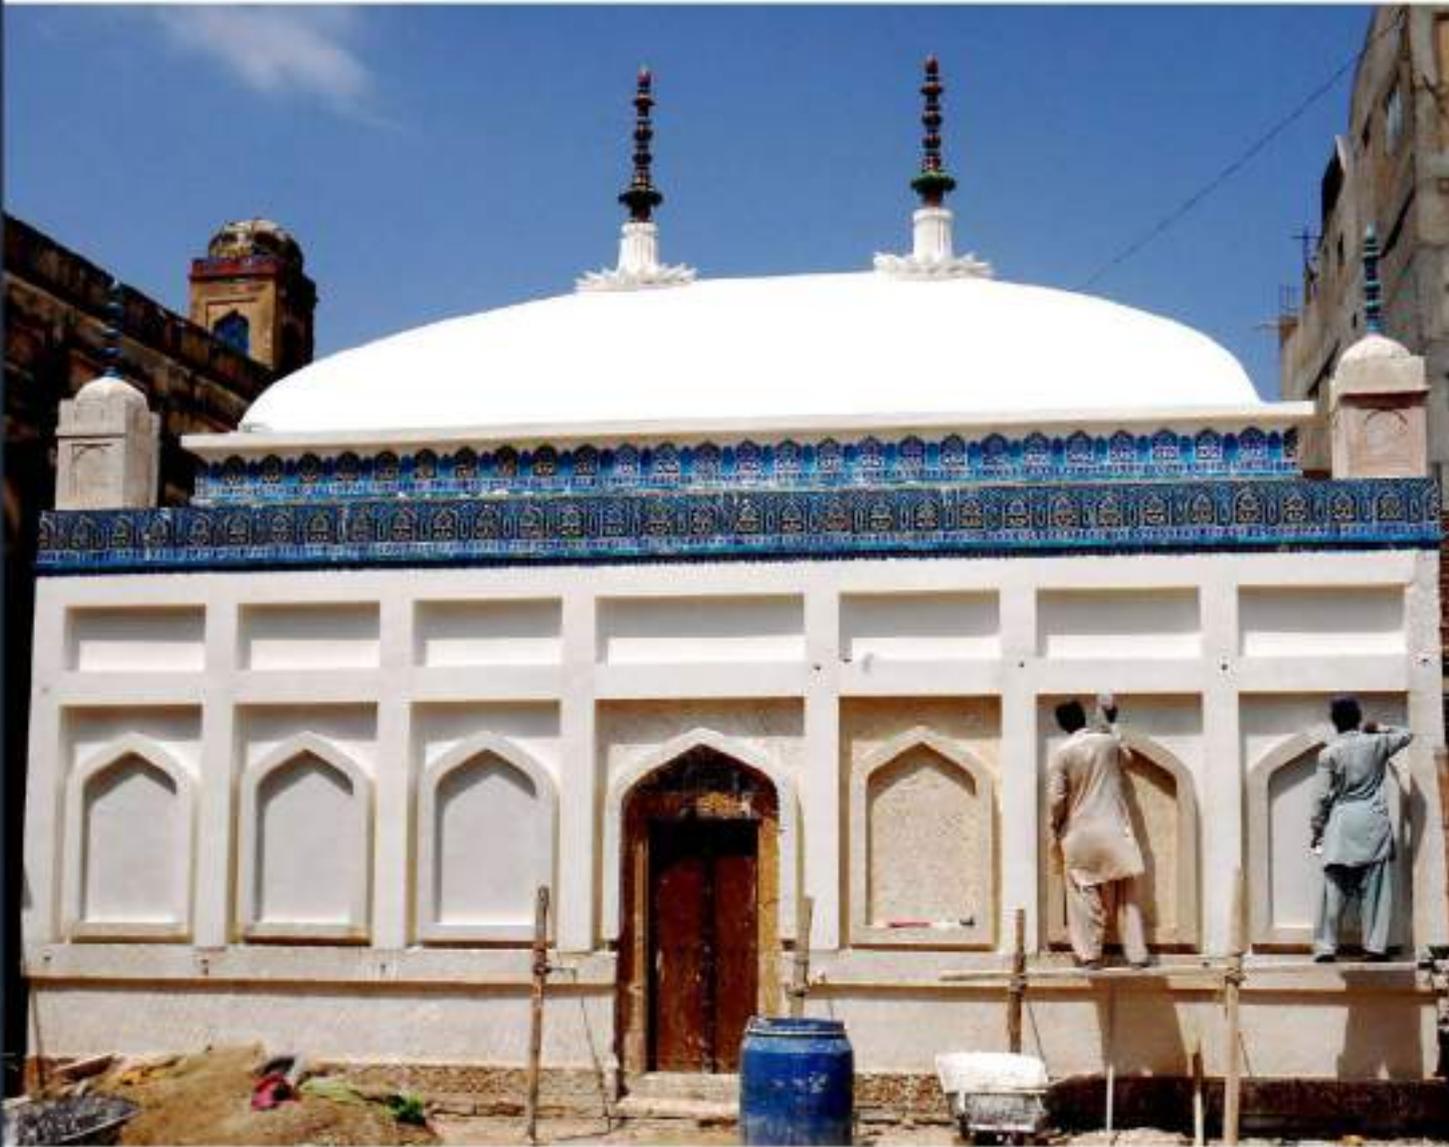

Tile Work at Facade of M4 is Completed , Plaster is in Progress

CONSERVATION PROGRESS


Mir Karam Ali Khan Talpur Tomb`s Complex



Western Side of Vaulted Roof Structure is Completed

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tombs (Complex)

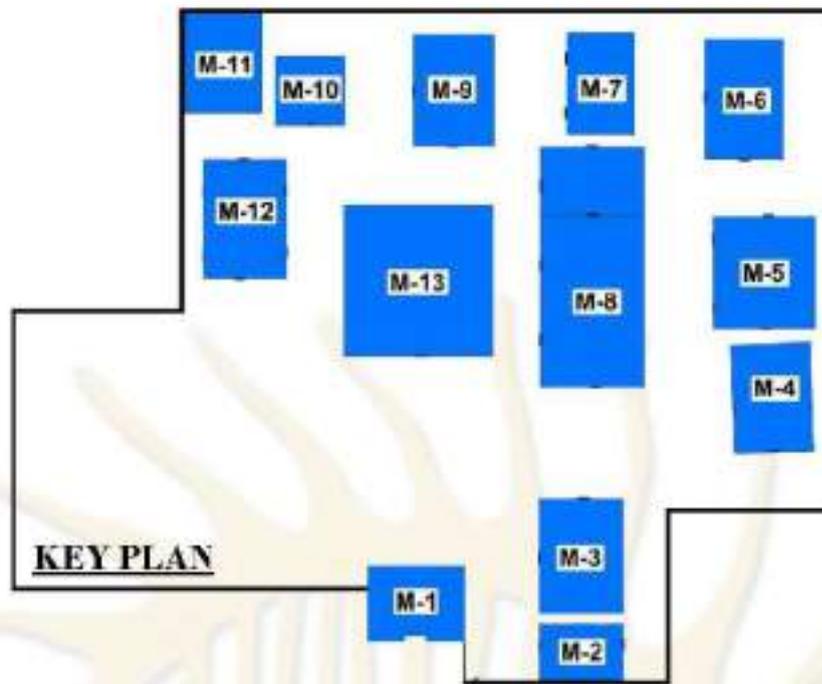

Mir Karam Ali Khan Talpur Tombs (Complex)

M-13 | Mir Karam Ali Khan Talpur Tomb

- Tile Work & Lime Plaster in Facade of Mir Karam Ali Khan Talpur Tomb is about Completed.
- Final Lime Plaster in kiosks of Mir Karam Ali Khan Talpur Tomb is completed, Seven Finial are fixed on Kiosk of Mir Karam Ali Khan Talpur Tomb.
- Chiroil, Lime Coating and Lime Plaster on the main arch of facade of Mir Karam Ali is completed.
- Turrets of Mir Karam Ali Khan Talpur are Completed.
- Northern Side of Mir Karam Ali Khan Talpur is 100% Completed.
- Arches of Northern Side of Mir Karam Ali Khan Talpur are re-fixed.
- Top Borders (Musalah) of Northern side of Mir Karam Ali Khan Talpur are completed.
- Final Lime Plaster of vertical & horizontal Borders are completed.
- Arches of Original kashi tiles at northern side of tomb are re-fixed.
- Kashi tiles beside top border (Musallah) on the northern side of Mir Karam Ali Khan Tomb are fixed.
- Old Kashi Tiles at the bottom (Izhoro) on the northern side of Mir Karam Ali Khan Talpur Tomb is re-fixed.
- Kashi tiles on the top border of southern side is restored.
- Kashi in arches on the southern side are completed.
- One Arch of the right bottom of Facade is replaced.

M-1 | Entrance Gate

- Eastern side of Main Entrance is 95% Completed.
- Western side of Main Entrance is also 95% Completed.

M-8 | Flat Roof Structure (Mir Naseer Khan Talpur's Tomb)

- Eastern side including Kiosks are 100% Completed.
- Kashi (Musalah) has been placed at the top of monument.
- Lime Plaster at the Borders at facade of monument is completed.
- Southern side of Mir Naseer Khan Talpur is 80% Completed.
- Kashi tiles on the horizontal panels (Tawez) on the top of structure are restored.

M-4 | Vaulted Roof Structure


- 90% Kashi Work is Completed of Tajjar which is located in Northern Side of Mir Naseer Khan Talpur.
- Chiroil & Lime Coating of Kiosks of Tajjar is completed.
- Lime Plaster at the top of vaulted roof is completed.
- Chiroli & Lime Coating of Base of Finial is completed.
- Two Finial at the top of vaulted roof are restored.
- Tiles are fixed on facade and also lime work is completed.
- Corner Turrets are restored on the facade of M4.

M-3 | Vaulted Roof Structure


- Fixing of Kashi Tiles at west side of "Tajjar" at north east side of Mir Karam Ali Tomb is completed.
- Lime plaster at the top of vaulted roof is completed.
- Fixing of kashi on the northern side of Tajjar is in progress.
- Kashi Work on top horizontal panels of "Tajjar" are Restored.

Mir Karam Ali Khan Talpur Tombs (Complex)

ENDOWMENT FUND TRUST | For the Preservation of the Heritage of Sindh

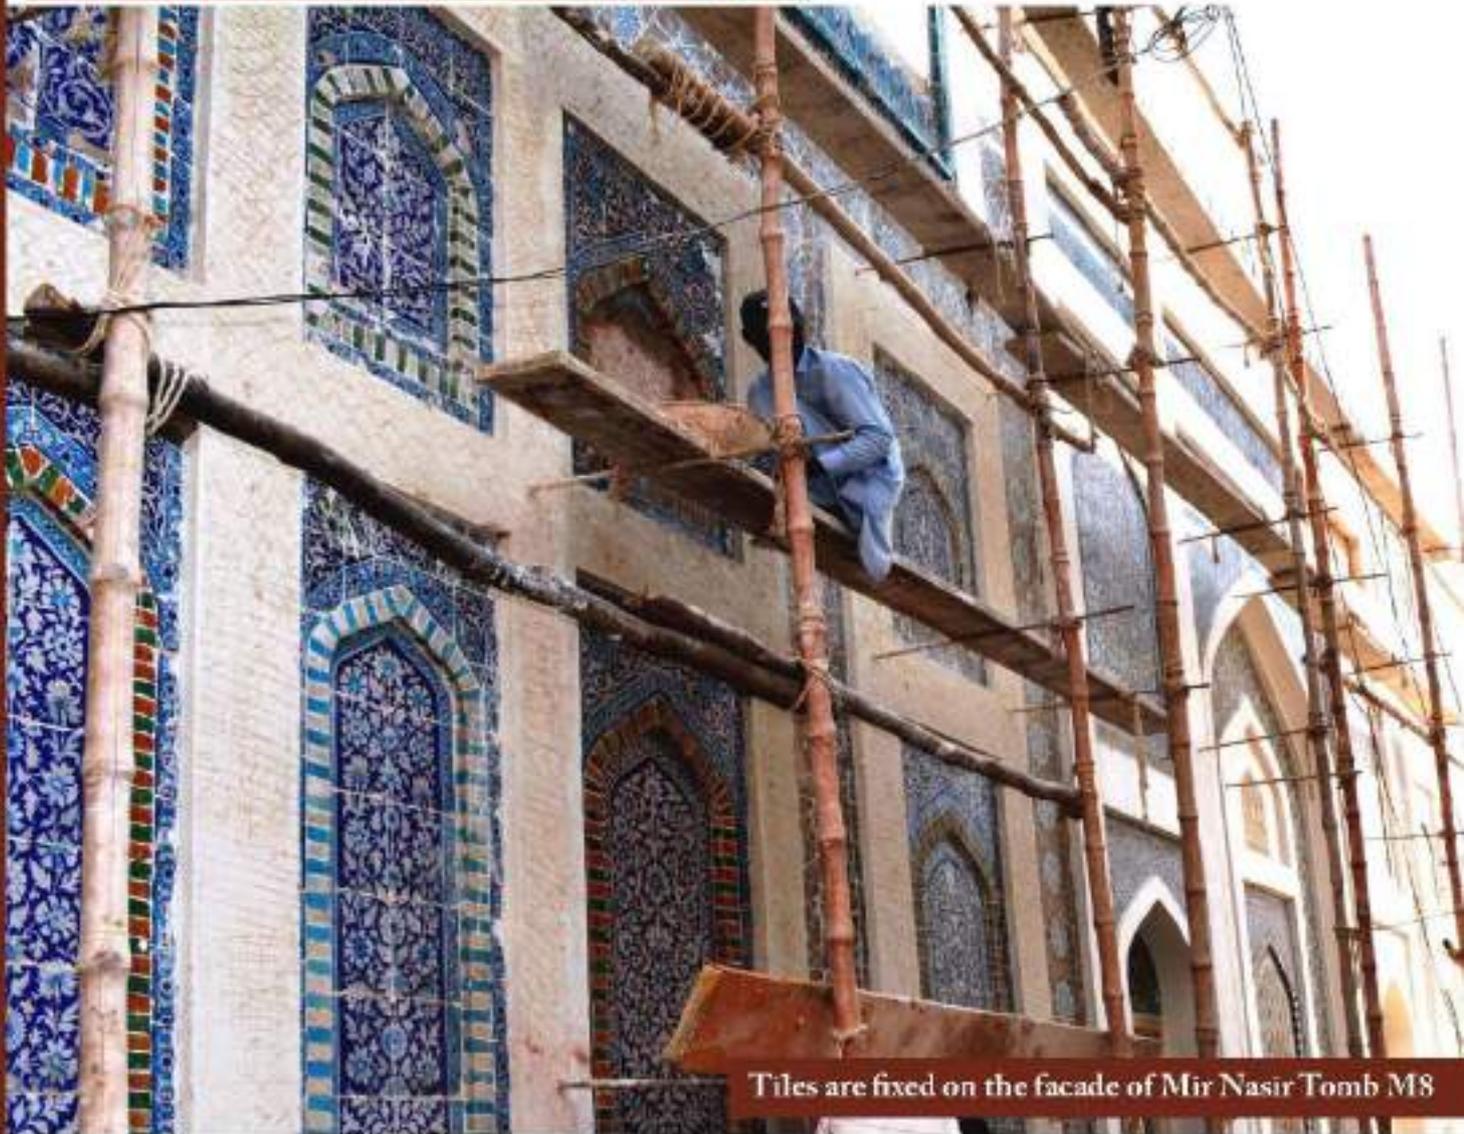

Tiles are fixed on the facade of Mir Nasir Tomb M8

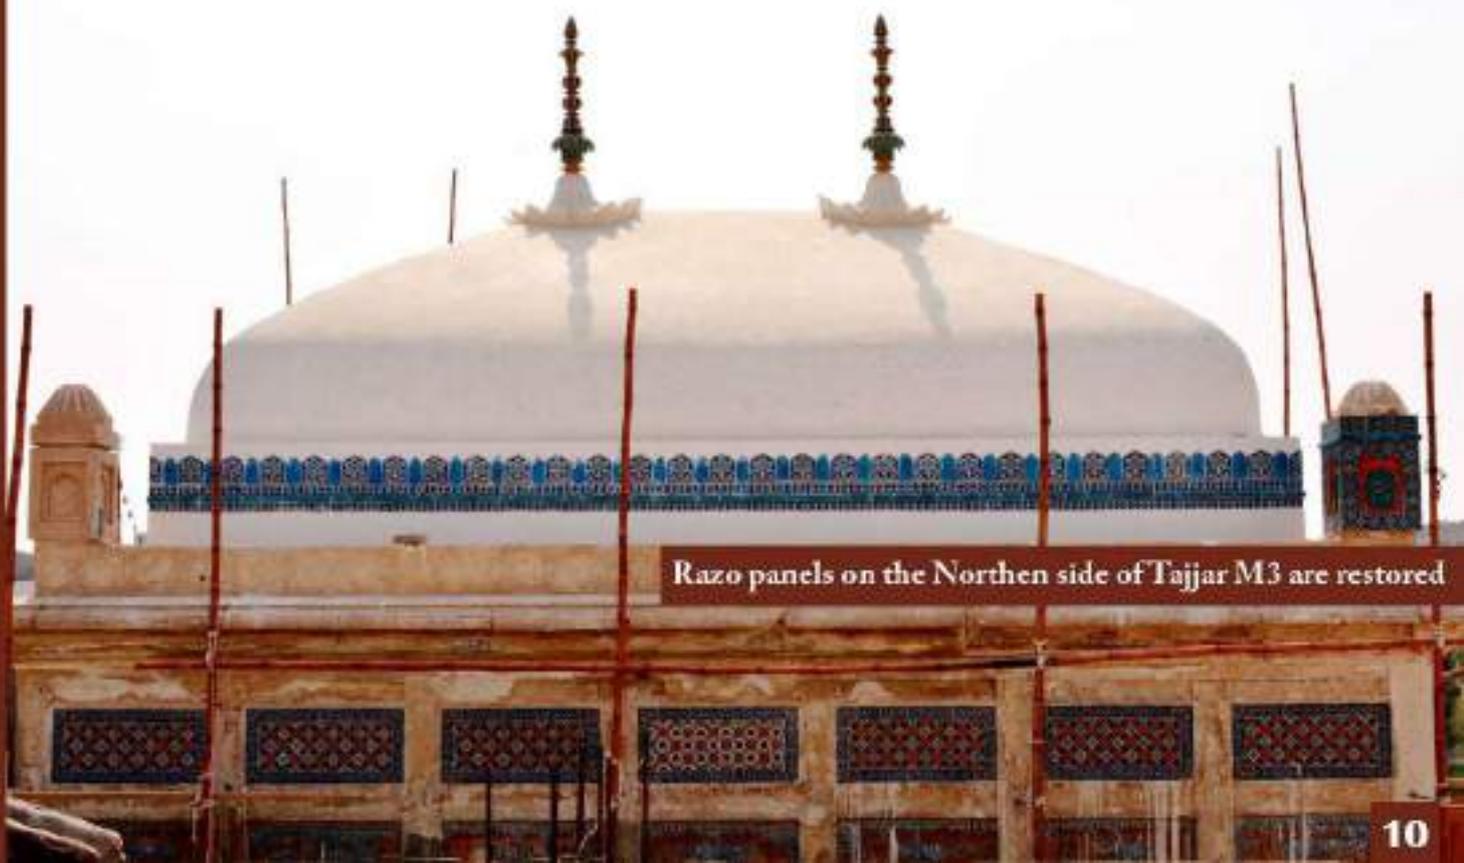

Razo panels on the Northern side of Tajar M3 are restored


CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tombs (Complex)

ENDOWMENT FUND TRUST | For the Preservation of the Heritage of Sindh




Corner Turrets are restored on the western side of Tajjar M3

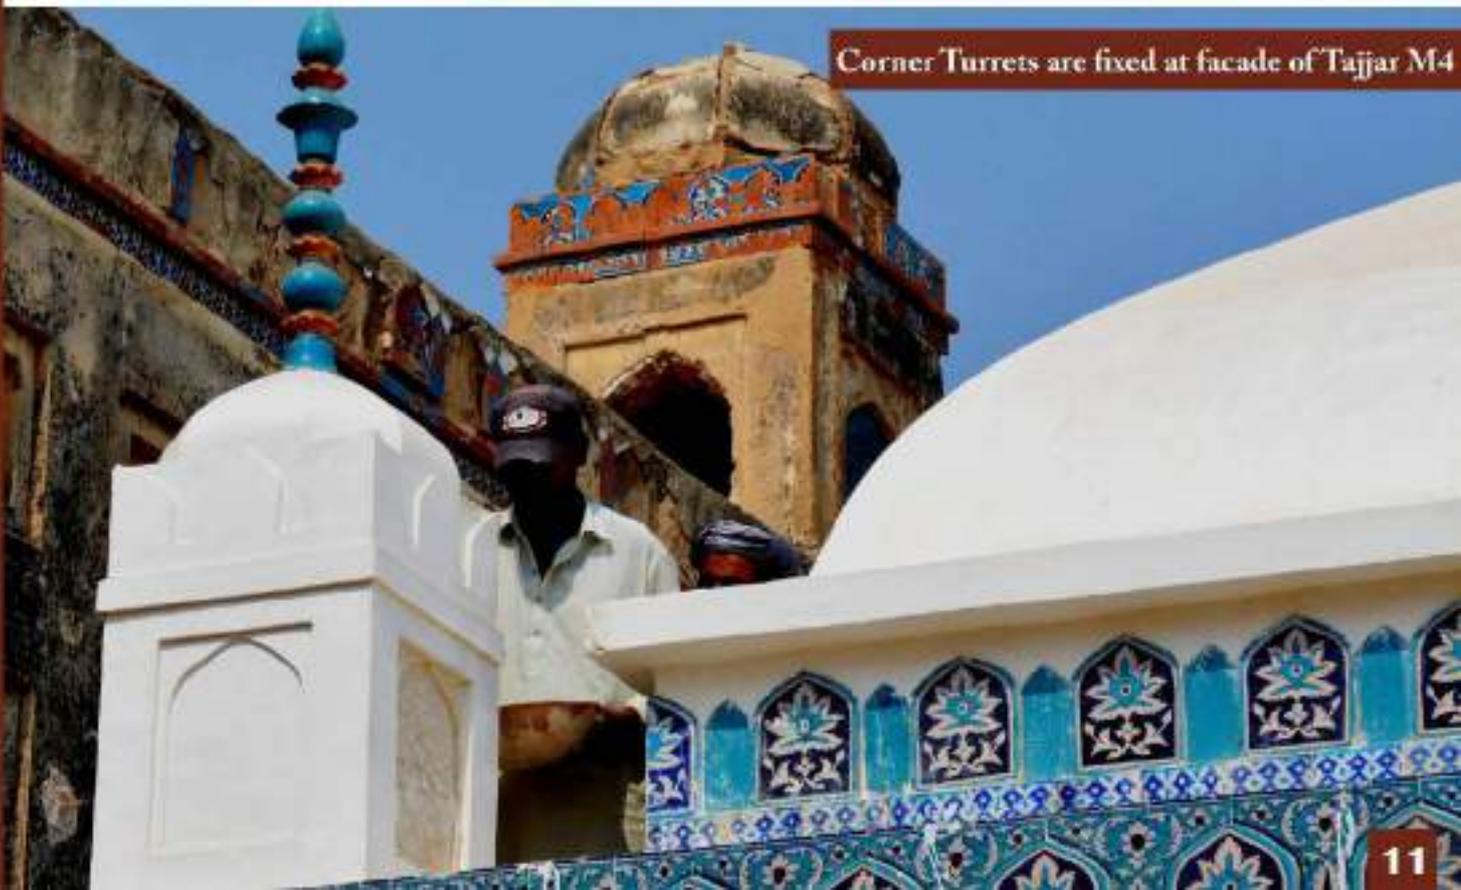


Corner Turrets are fixed at facade of Tajjar M4

Mir Karam Ali Khan Talpur Tombs (Complex)

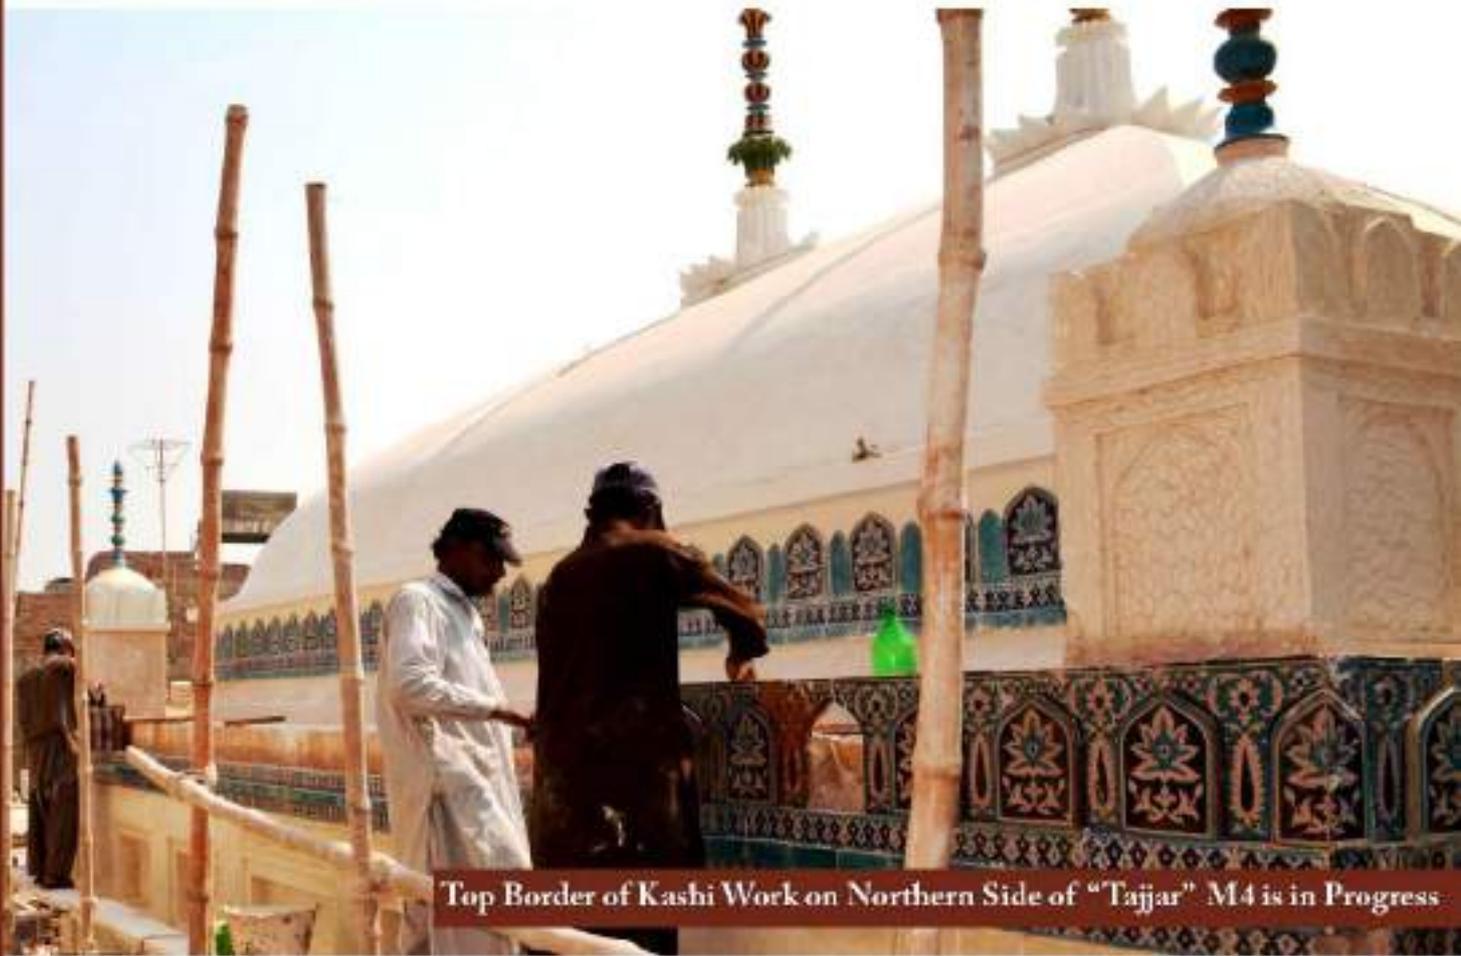

Top Border of Kashi Work on Northern Side of "Tajjar" M4 is in Progress

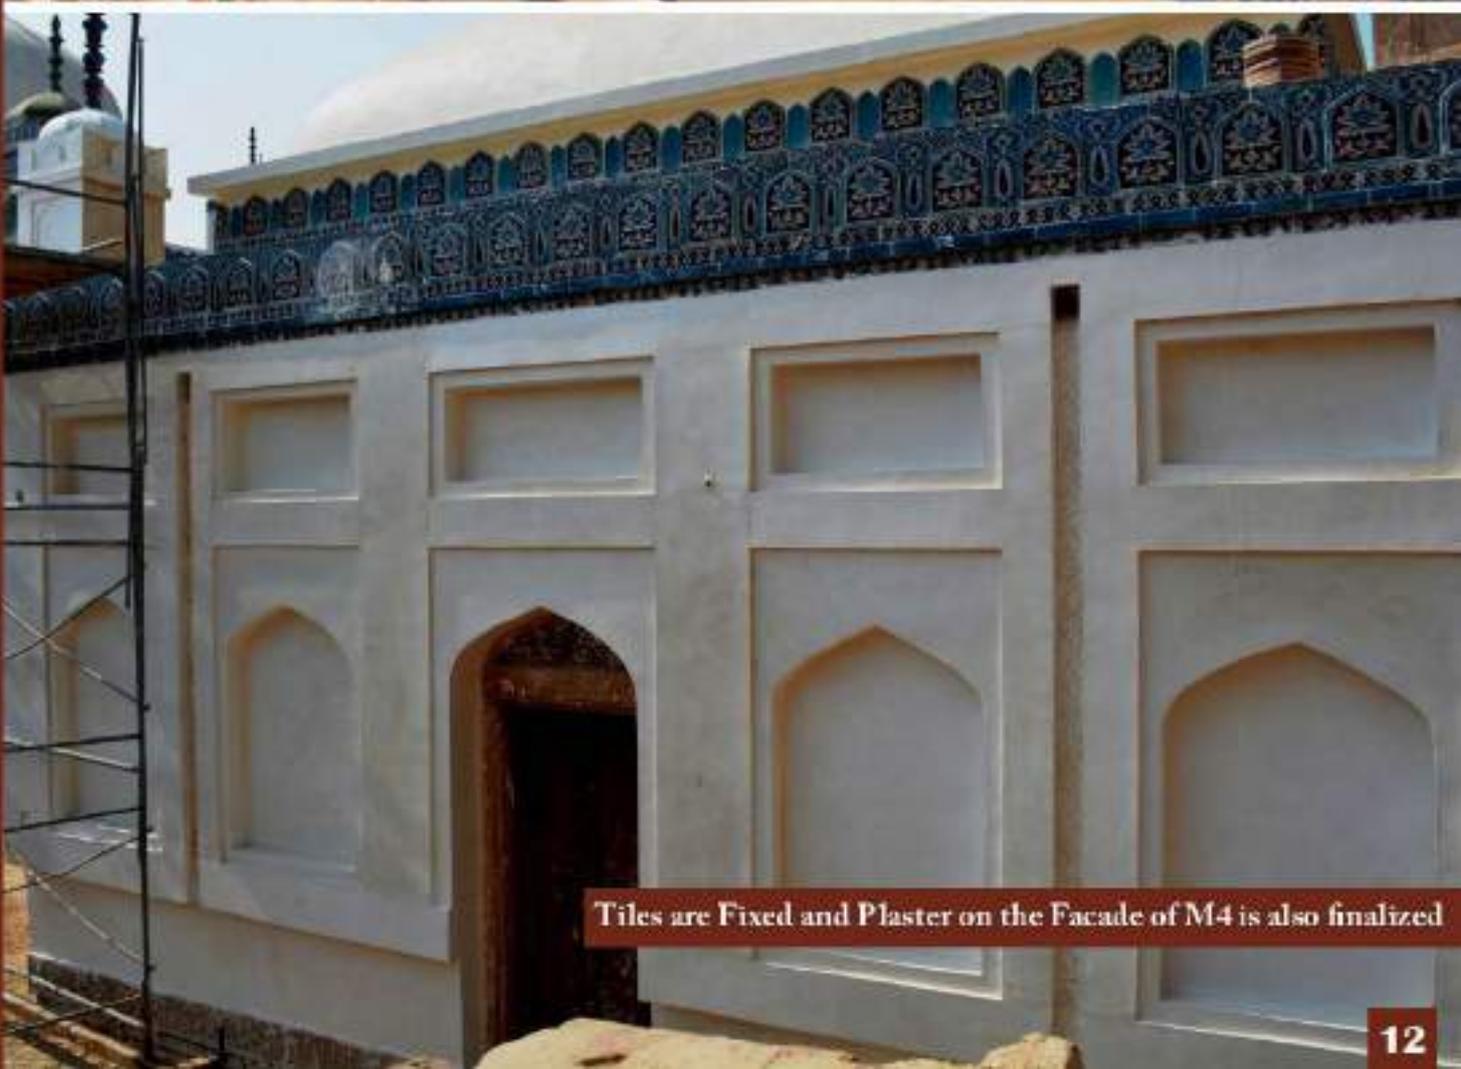

Tiles are Fixed and Plaster on the Facade of M4 is also finalized


Mir Karam Ali Khan Talpur Tombs (Complex)



For visitors, information board are fixed

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tombs (Complex)

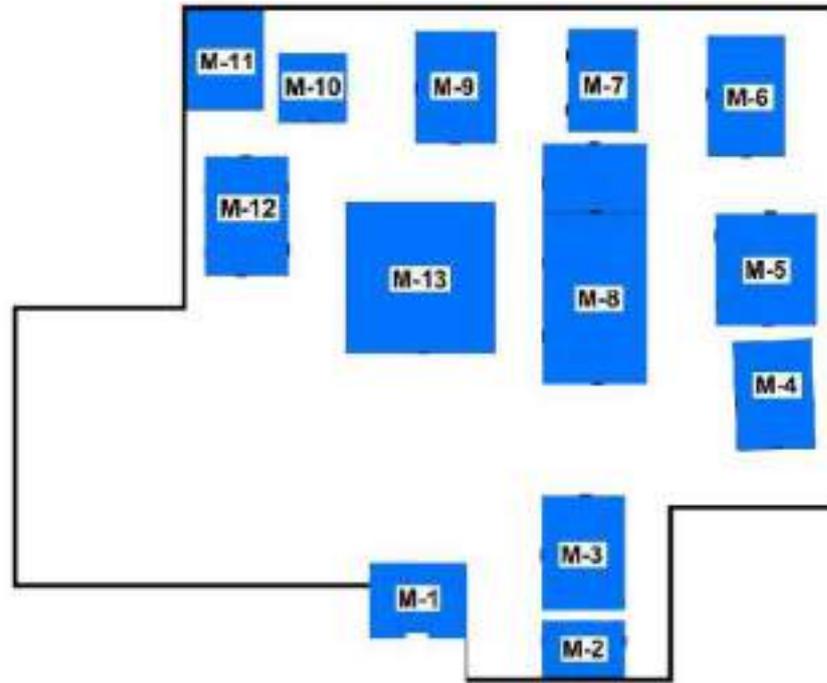

Mir Karam Ali Khan Talpur Tombs (Complex)

M-13 | Mir Karam Ali Khan Talpur Tomb

- Tile Work & Lime Plaster in Facade of Mir Karam Ali Khan Talpur Tomb is about Completed.
- Final Lime Plaster in kiosks of Mir Karam Ali Khan Talpur Tomb is completed, All Finial are fixed on Kiosk of Mir Karam Ali Khan Talpur Tomb.
- Chiroll, Lime Coating and Lime Plaster on the main arch of facade of Mir Karam Ali is finalized.
- Turrents of Mir Karam Ali Khan Talpur are restored.
- Northern Side of Mir Karam Ali Khan Talpur is Completed.
- Arches of Northern Side of Mir Karam Ali Khan Talpur are re-fixed.
- Top Borders (Musalah) of Northern side of Mir Karam Ali Khan Talpur are completed.
- Arches of Original kashi tiles at northern side of tomb are re-fixed.
- Kashi tiles beside top border (Musallah) on the northern side of Mir Karam Ali Khan Tomb are fixed.
- Old Kashi Tiles at the bottom (Izhoro) on the northern side of Mir Karam Ali Khan Talpur Tomb is re-fixed.
- Kasha tiles on the top border of southern side is restored.
- Kashi in arches on the southern side are completed.
- One Arch of the right bottom of Facade is replaced.
- Southern side of Tomb is also completed.
- Western side of Tomb plastered and tiles are fixed.

M-1 | Entrance Gate

- Eastern side of Main Entrance is 95% Completed.
- Western side of Main Entrance is also 95% Completed.
- Lime coating on the northern side is in progress.

M-8 | Flat Roof Structure (Mir Naseer Khan Talpur's Tomb)

- Eastern side including Kiosks are 100% Completed.
- Kashi (Musalah) has been placed at the top of monument.
- Lime Plaster at the Borders at facade of monument is completed.
- Southern side of Mir Naseer Khan Talpur is 100% Completed.
- Kashi tiles on the horizontal panels (Tawez) on the top of structure are restored.
- Chiroll and Lime coating on the Northern side of Tomb is in progress.
- Finial are fixed on the restored kiosk of Mir Naseer Khan Talpur's Tomb.

M-4 | Vaulted Roof Structure

- Kashi Work is Completed of Tajjar wich is located in Northern Side of Mir Naseer Khan Talpur.
- Chiroll & Lime Coating tiles are fixed of Kiosks of Tajjar.
- Lime Plaster at the top of vaulted roof is completed.
- Chiroll & Lime Coating of Base of Finial is completed.
- Two Finial at the top of vaulted roof are restored.
- Tiles are fixed on facade and also lime work is completed.
- Corner Turrents are restored on the facade of M4.

M-3 | Vaulted Roof Structure

- Lime plaster and tile work on facade of M3 are fully restored
- Fixing of Kashi Tiles at west side of "Tajjar" at north east side of Mir Karam Ali Tomb is completed.
- Lime plaster at the top of vaulted roof is completed.
- Fixing of kashi on the northern side of Tajjar is in finalized.
- Kashi Work on top horizontal panels of "Tajjar" are Restored.
- Chiroll and Lime coating on the North side is in progress.


M-2 | Small Flat Roof Structure

- Chiroll and Lime coating on two facade of M-2 is in progress.

CONSERVATION PROGRESS


Mir Karam Ali Khan Talpur Tombs (Complex)

BEFORE

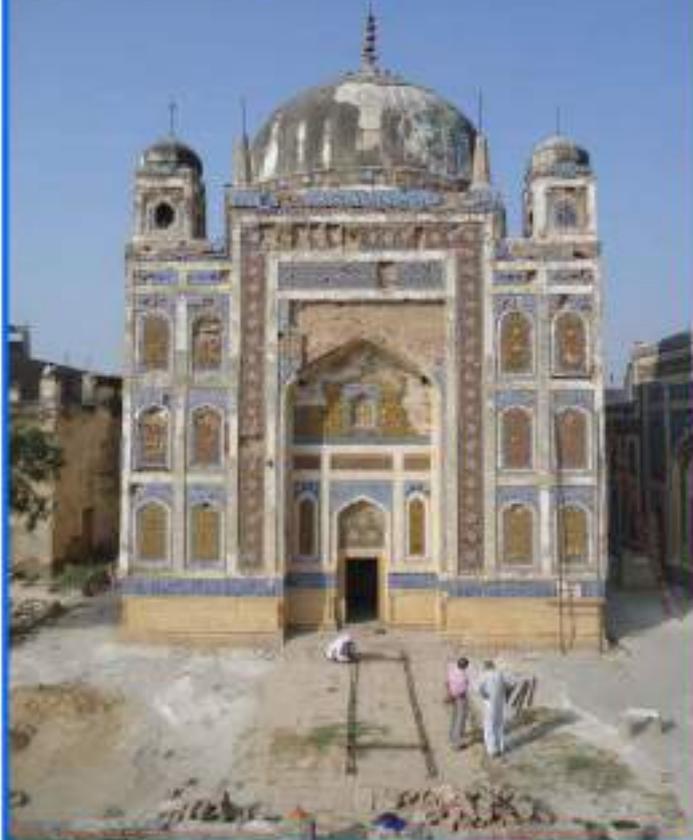

Before Mir Karam Ali Khan Talpur's Tomb M-13

AFTER

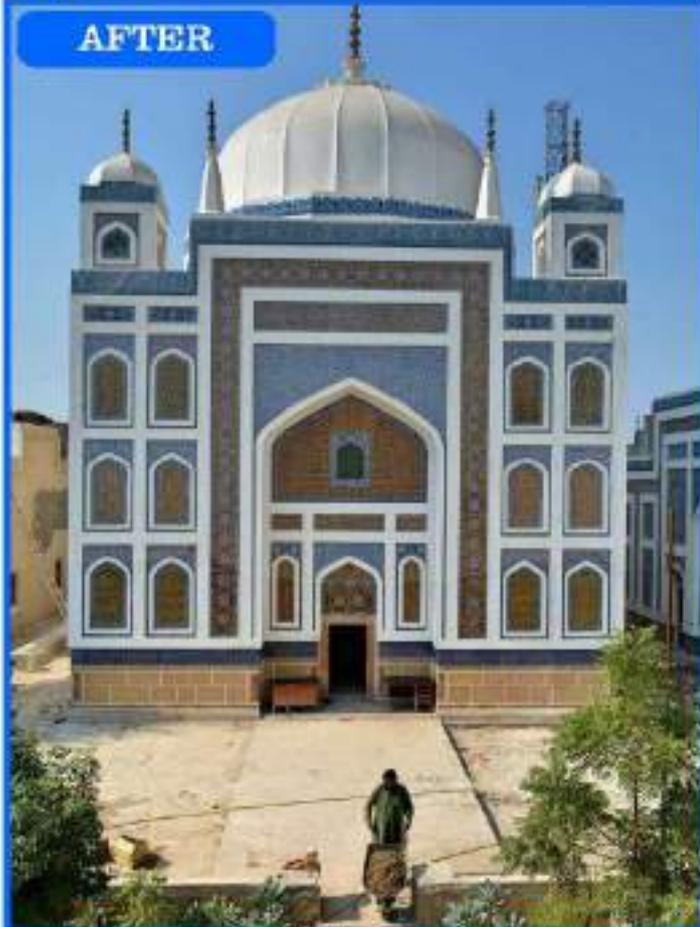

After Mir Karam Ali Khan Talpur's Tomb M-13

BEFORE



Before Mir Naseer Khan Talpur's Tomb M-8

AFTER



After Mir Naseer Khan Talpur's Tomb M-8

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tombs (Complex)

BEFORE



Main Entrance Gate M-1

AFTER



Main Entrance Gate M-1 | After

Mir Karam Ali Khan Talpur Tombs (Complex)




Restoration of fresco work inner dome of entrance gate M-1



Chiropoli and lime coating on the Northern Side of Mir Naseer Khan Talpur's Tomb M-8

Mir Karam Ali Khan Talpur Tombs (Complex)

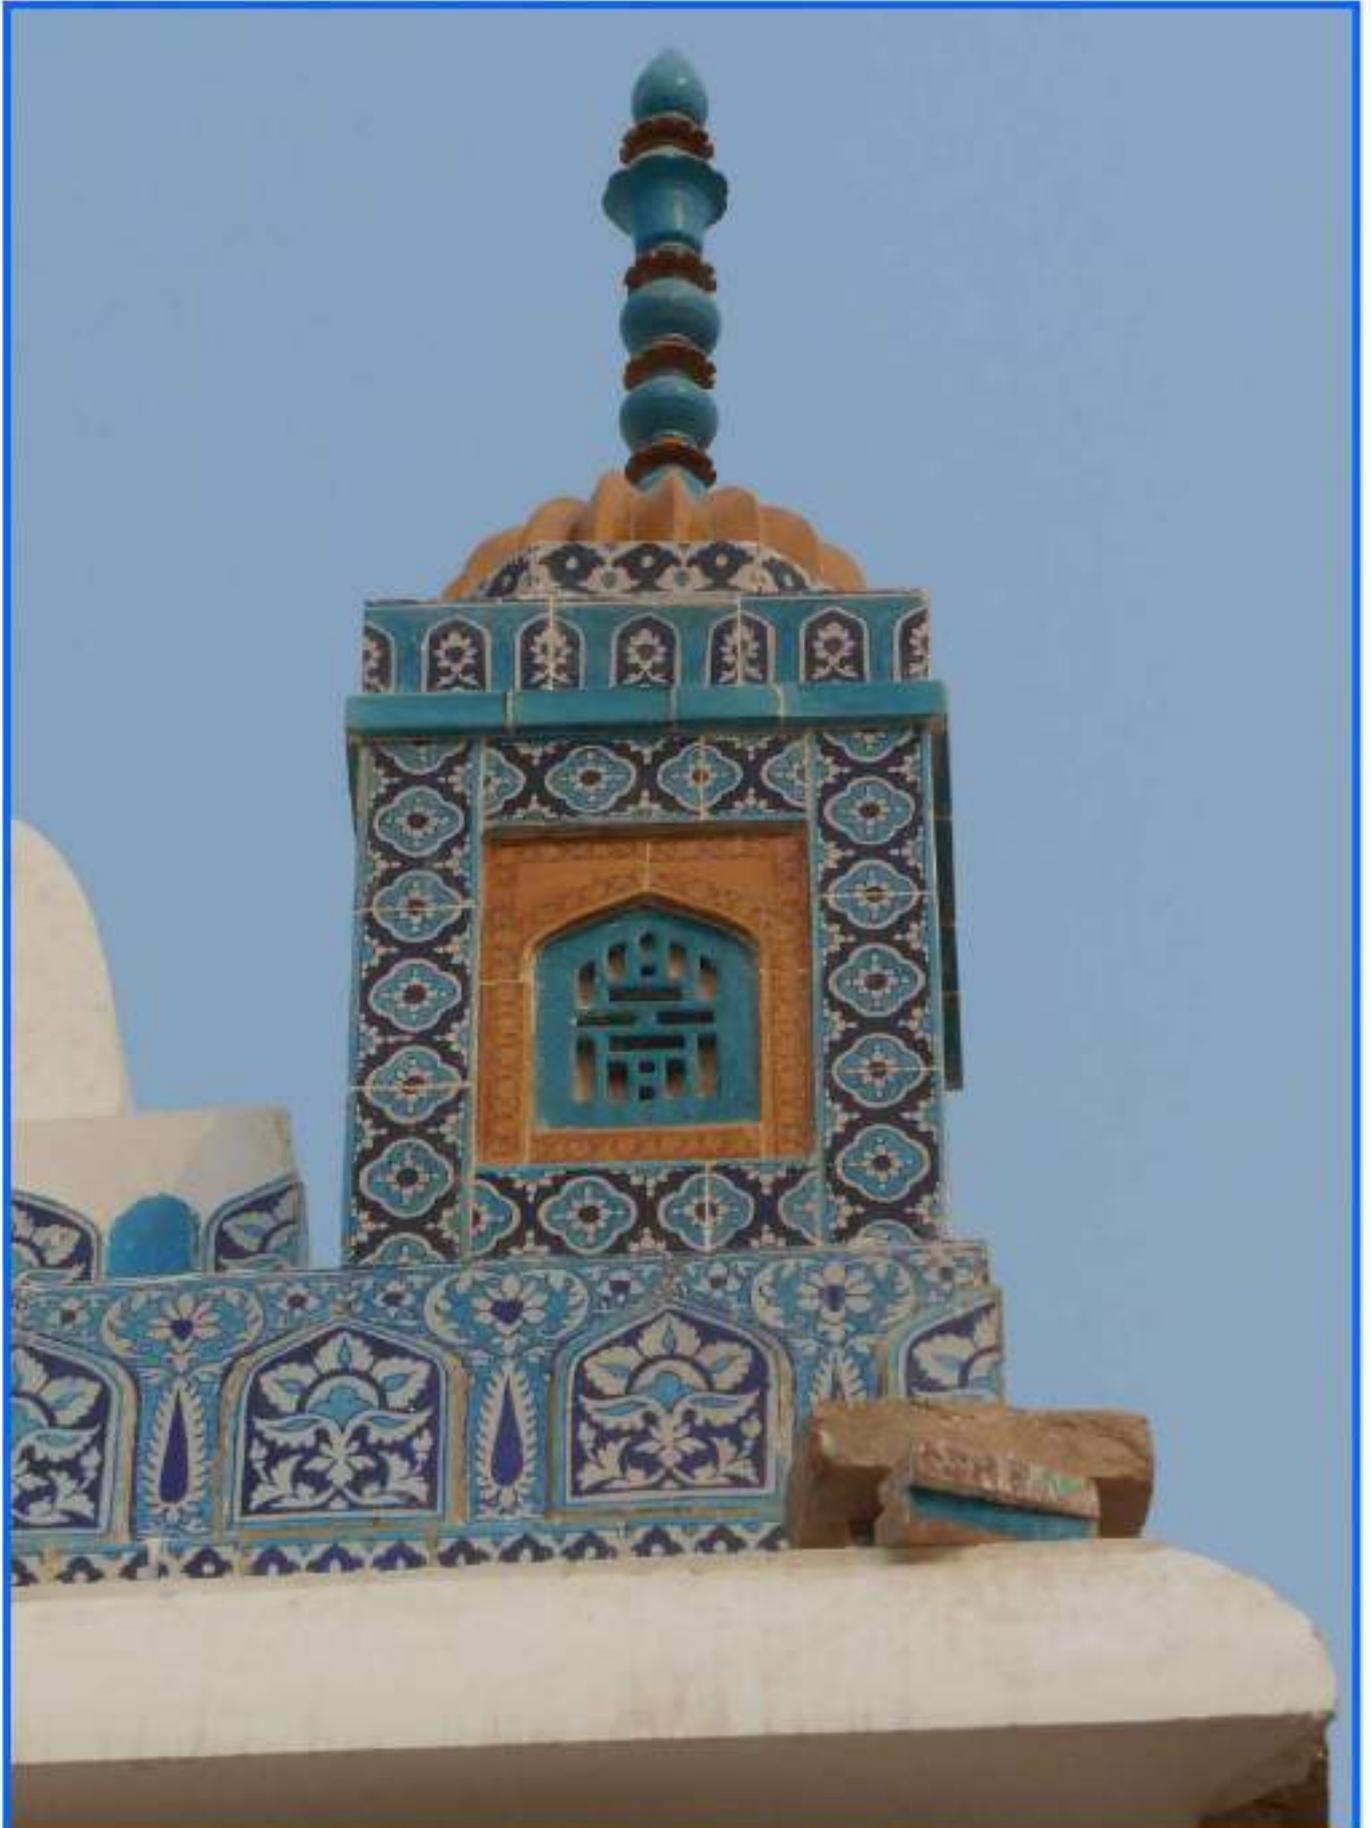

Finial of M-8 Flat Roof Structure (Mir Naseer Khan Talpur) is restored

Mir Karam Ali Khan Talpur Tombs (Complex)



Chiroli and lime coating on the Northern Side of vaulted roof structure M-3 is in progress

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tombs (Complex)

BEFORE



Vaulted roof structure M-4 "Tajjar"


AFTER



Vaulted roof structure M-4 "Tajjar"

Mir Karam Ali Khan Talpur Tombs (Complex)

BEFORE

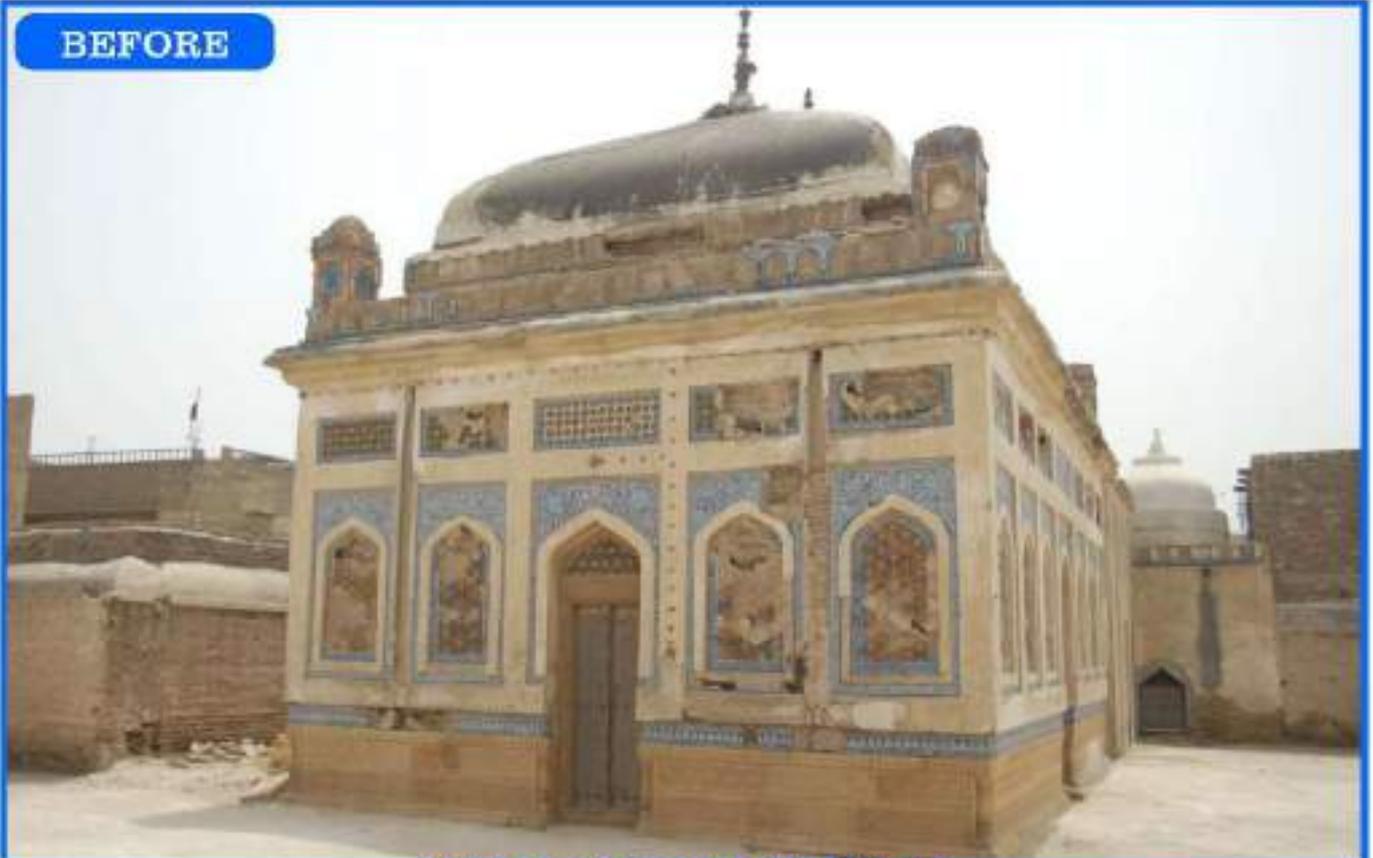

Vaulted roof structure M-3 "Tajjar"

AFTER



Vaulted roof structure M-3 "Tajjar"

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tombs (Complex)

BEFORE



Vaulted roof structure M-4 "Tajjar"


AFTER



Vaulted roof structure M-4 "Tajjar"

CONSERVATION PROGRESS

Mir Karam Ali Khan Talpur Tombs (Complex)

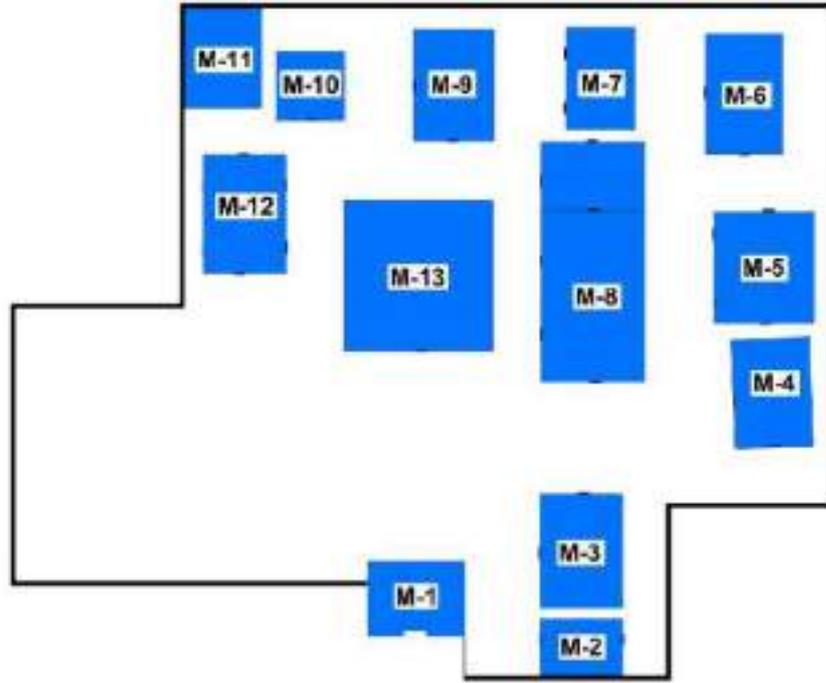

Mir Karam Ali Khan Talpur Tombs (Complex)

M-13 | Mir Karam Ali Khan Talpur Tomb

- Tile Work & Lime Plaster in Facade of Mir Karam Ali Khan Talpur Tomb is Completed.
- Final Lime Plaster in kiosks of Mir Karam Ali Khan Talpur Tomb is completed, All Finial are fixed on Kiosk of Mir Karam Ali Khan Talpur Tomb.
- Chiroll, Lime Coating and Lime Plaster on the main arch of facade of Mir Karam Ali is finalized.
- Turrents of Mir Karam Ali Khan Talpur are restored.
- Northern Side of Mir Karam Ali Khan Talpur is Completed.
- Arches of Northern Side of Mir Karam Ali Khan Talpur are re-fixed.
- Top Borders (Musalah) of Northern side of Mir Karam Ali Khan Talpur are completed.
- Arches of Original kashi tiles at northern side of tomb are re-fixed.
- Kashi tiles beside top border (Musallah) on the northern side of Mir Karam Ali Khan Tomb are fixed.
- Old Kashi Tiles at the bottom (Izhoro) on the northern side of Mir Karam Ali Khan Talpur Tomb is re-fixed.
- Kasha tiles on the top border of southern side is restored.
- Kashi in arches on the southern side are completed.
- One Arch of the right bottom of Facade is replaced.
- Southern side of Tomb is also completed.
- Western side of Tomb plastered and tiles are fixed.
- Fresco work on the inner wall of the tomb is in momentum.

M-1 | Entrance Gate

- Eastern side of Main Entrance is Completed.
- Western side of Main Entrance is also Completed.
- Lime coating on the northern side is in Completed.
- Two walls of entrance of main gate is plastered.
- fresco work on the inner dome of main entrances is in advancement.

M-8 | Flat Roof Structure (Mir Naseer Khan Talpur`s Tomb)

- Eastern side including Kiosks are Completed.
- Kashi (Musalah) has been placed at the top of monument.
- Lime Plaster at the Borders at facade of monument is completed.
- Southern side of Mir Naseer Khan Talpur is Completed.
- Kashi tiles on the horizontal panels (Tawez) on the top of structure are restored.
- Chirolli and Lime coating on the Northern side of Tomb is in progress.
- Finial are fixed on the restored kiosk of Mir Naseer Khan Talpur's Tomb.
- Restoration of Kashi tiles on the northern side is in progress.

M-4 | Vaulted Roof Structure

- Kashi Work of Tajjar M-4 on the Northern Side of Mir Naseer Khan Talpur is completed.
- Chirolli & Lime Coating and tiles are fixed of Kiosks of Tajjar.
- Lime Plaster at the top of vaulted roof is completed.
- Chirolli & Lime Coating of Base of Finial is completed.
- Two Finial at the top of vaulted roof are restored.
- Tiles are fixed on facade and also lime work is completed.
- Corner Turrents are restored on the facade of M4.

M-3 | Vaulted Roof Structure

- Lime plaster and tile work on facade of M3 are fully restored
- Fixing of Kashi Tiles at west side of "Tajjar" is completed.
- Lime plaster at the top of vaulted roof is completed.
- Kashi Work on top horizontal panels of "Tajjar" are Restored.
- Chirolli and Lime coating on the North side is in progress.
- Re-fixing of Kashi tiles on the northern side is in progress.

Mir Karam Ali Khan Talpur Tombs (Complex)

M-2 | Flat Roof Small Structure

- Chiroli and Lime coating on facade of M-2 is ended.
- Chiroli and Lime coating on the top and northern side is finalized.


M-6 | Tajar

- Kashi are fixed on the top horizontal panels of facade M-6.
- Kashi tiles on the top of horizontal panels of northern side of M-6 is finished.




Facade of flat roof small structure M-2

Mir Karam Ali Khan Talpur Tombs (Complex)

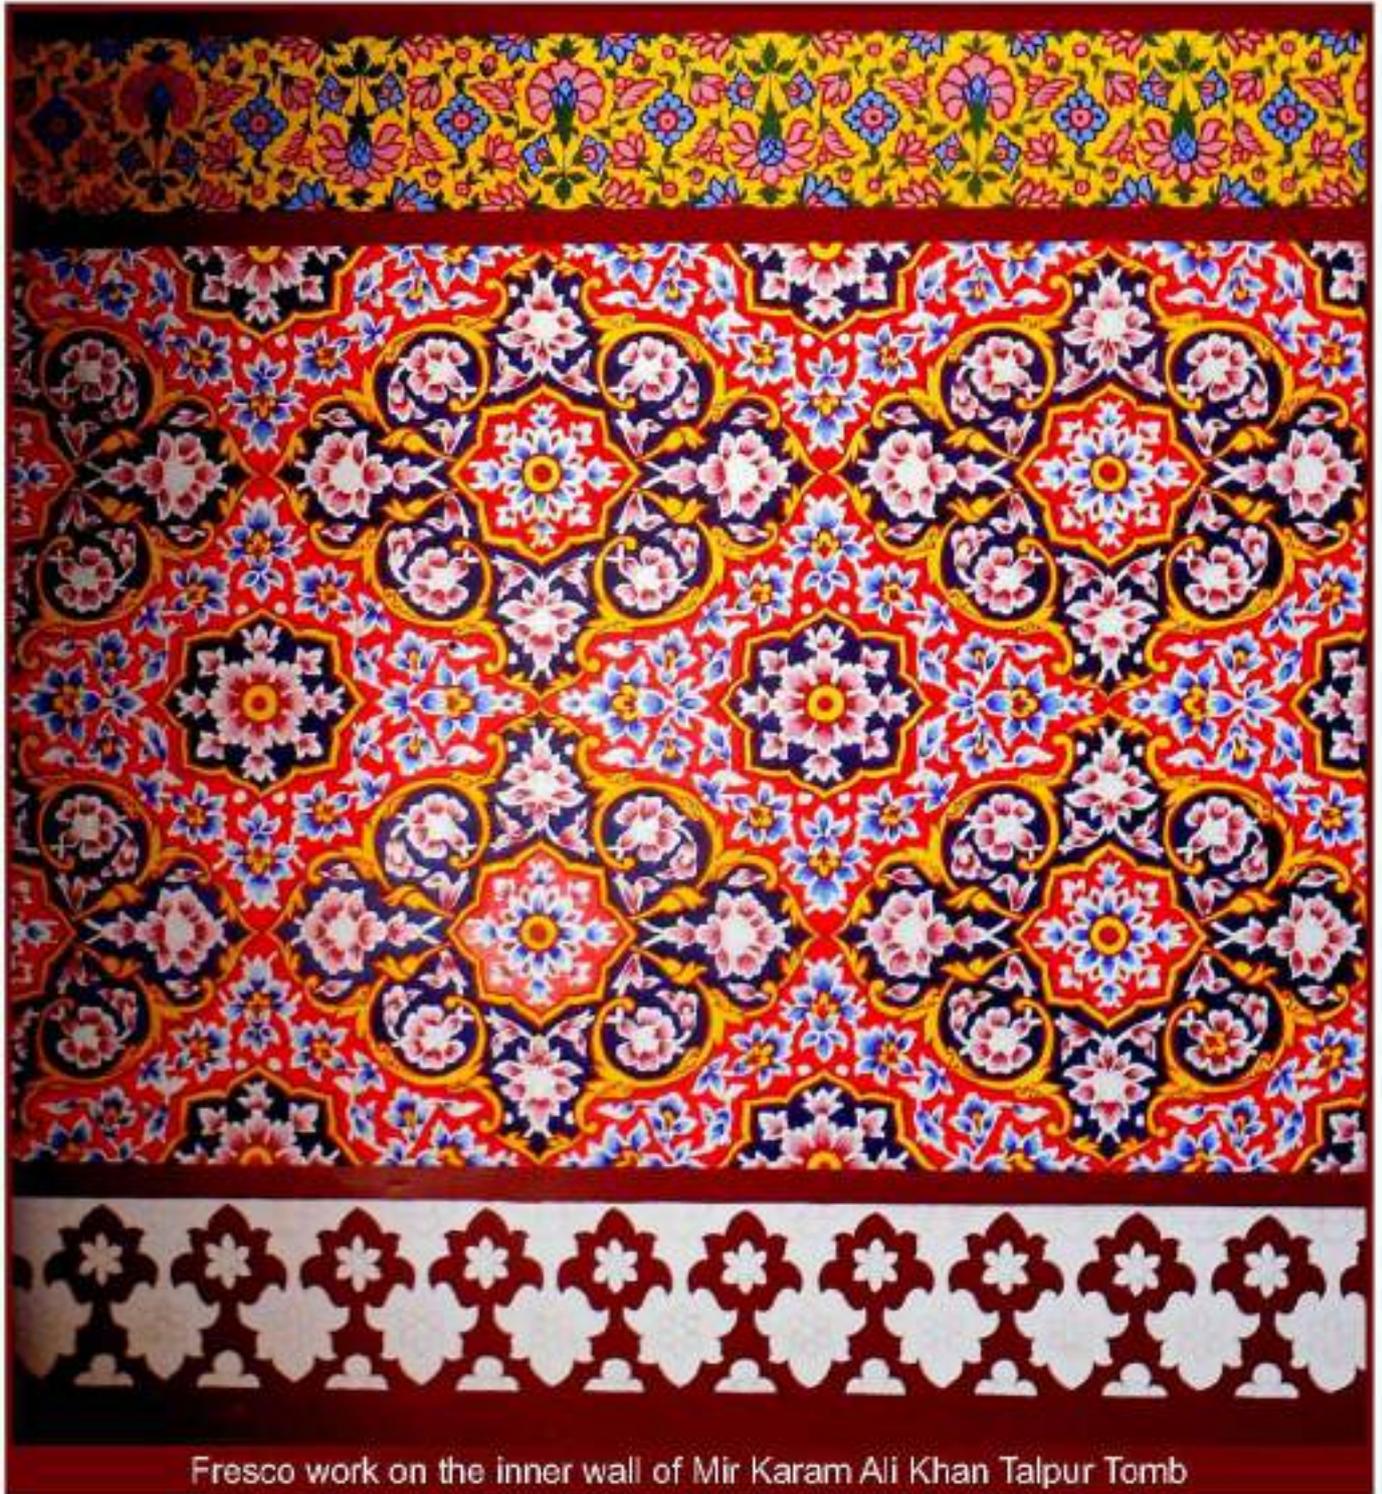

Fresco work on the inner wall of Mir Karam Ali Khan Talpur Tomb

Mir Karam Ali Khan Talpur Tombs (Complex)

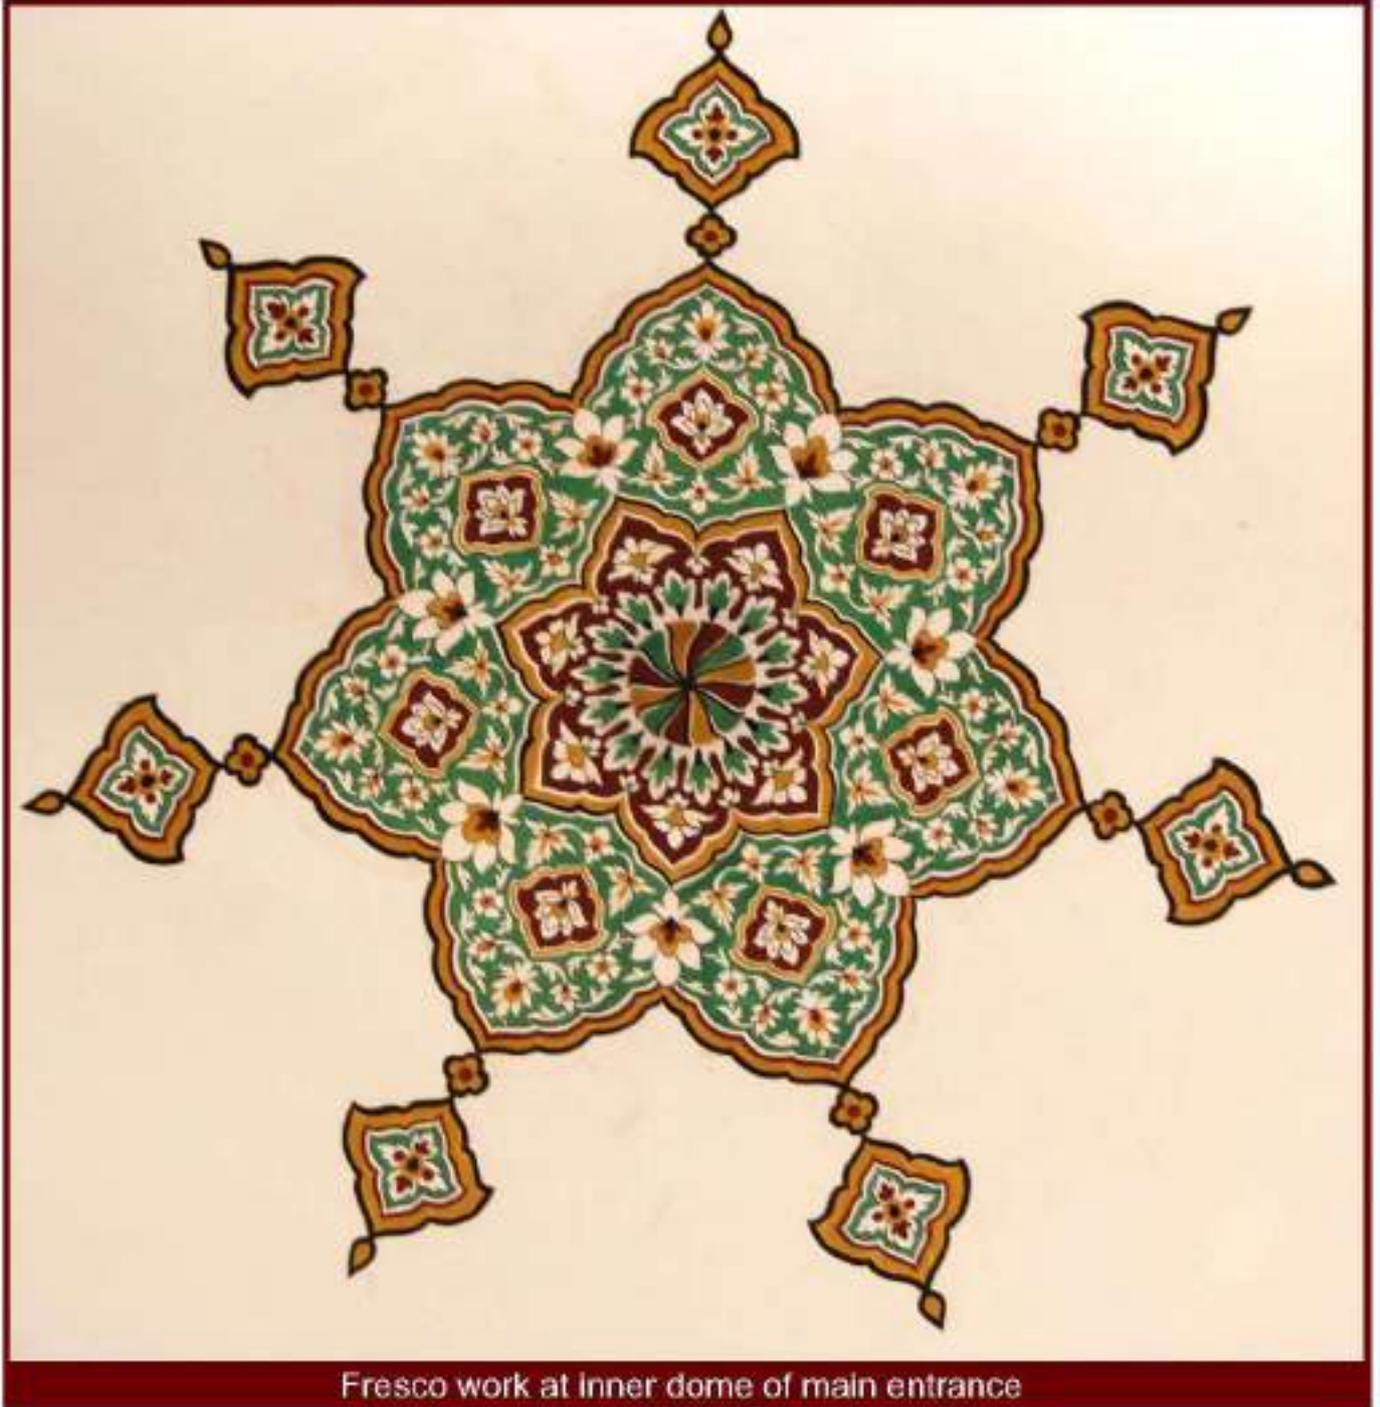


Fresco work at inner dome of main entrance

Mir Karam Ali Khan Talpur Tombs (Complex)



Border at bottom of facade of Mir Naseer Khan Tomb

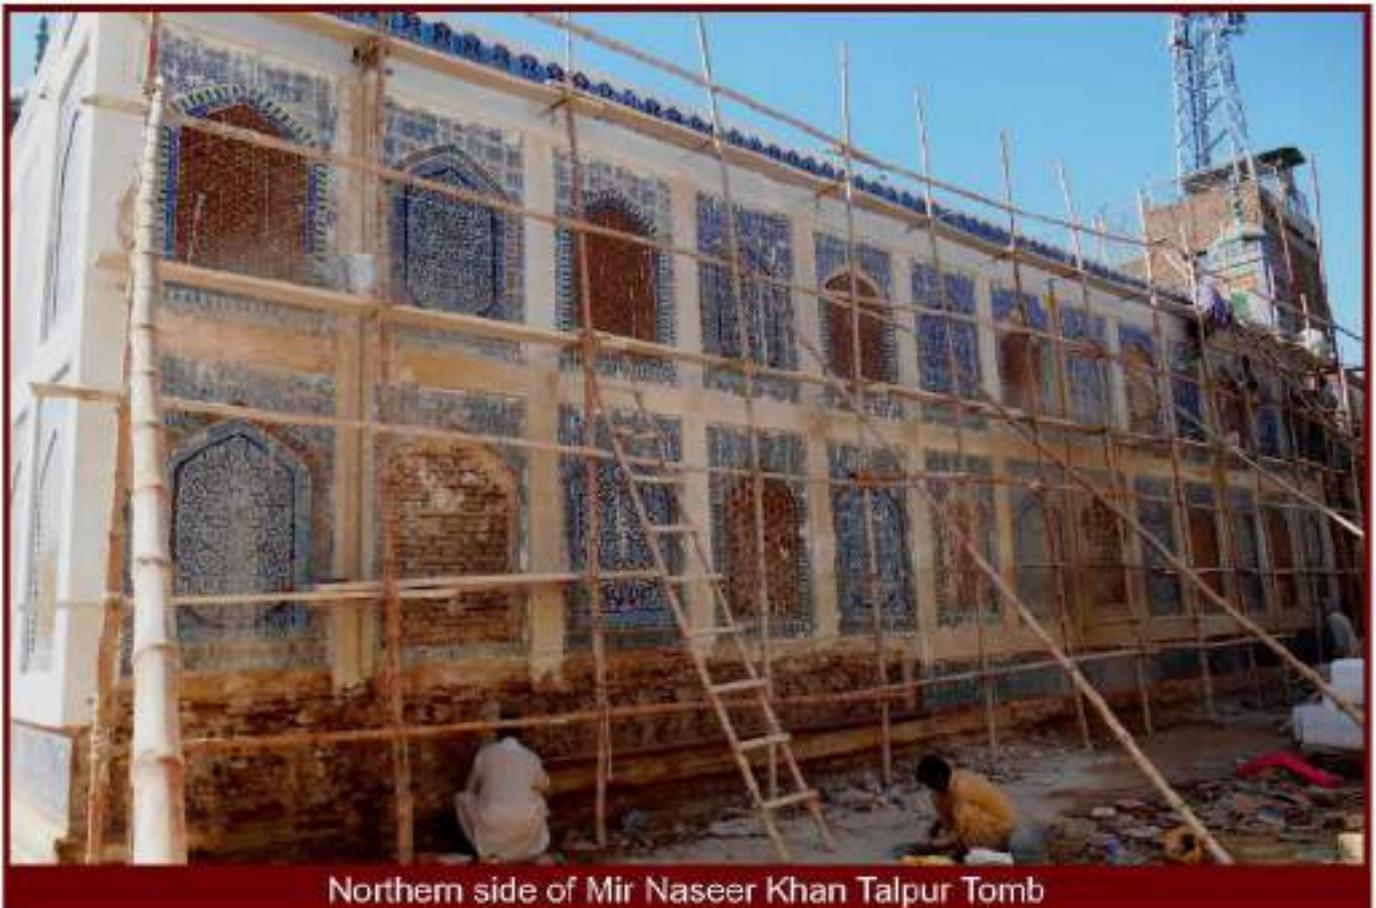


Northern side of Mir Naseer Khan Talpur Tomb

Mir Karam Ali Khan Talpur Tombs (Complex)




Panels are fixed on the northern side of Tajjar M-6

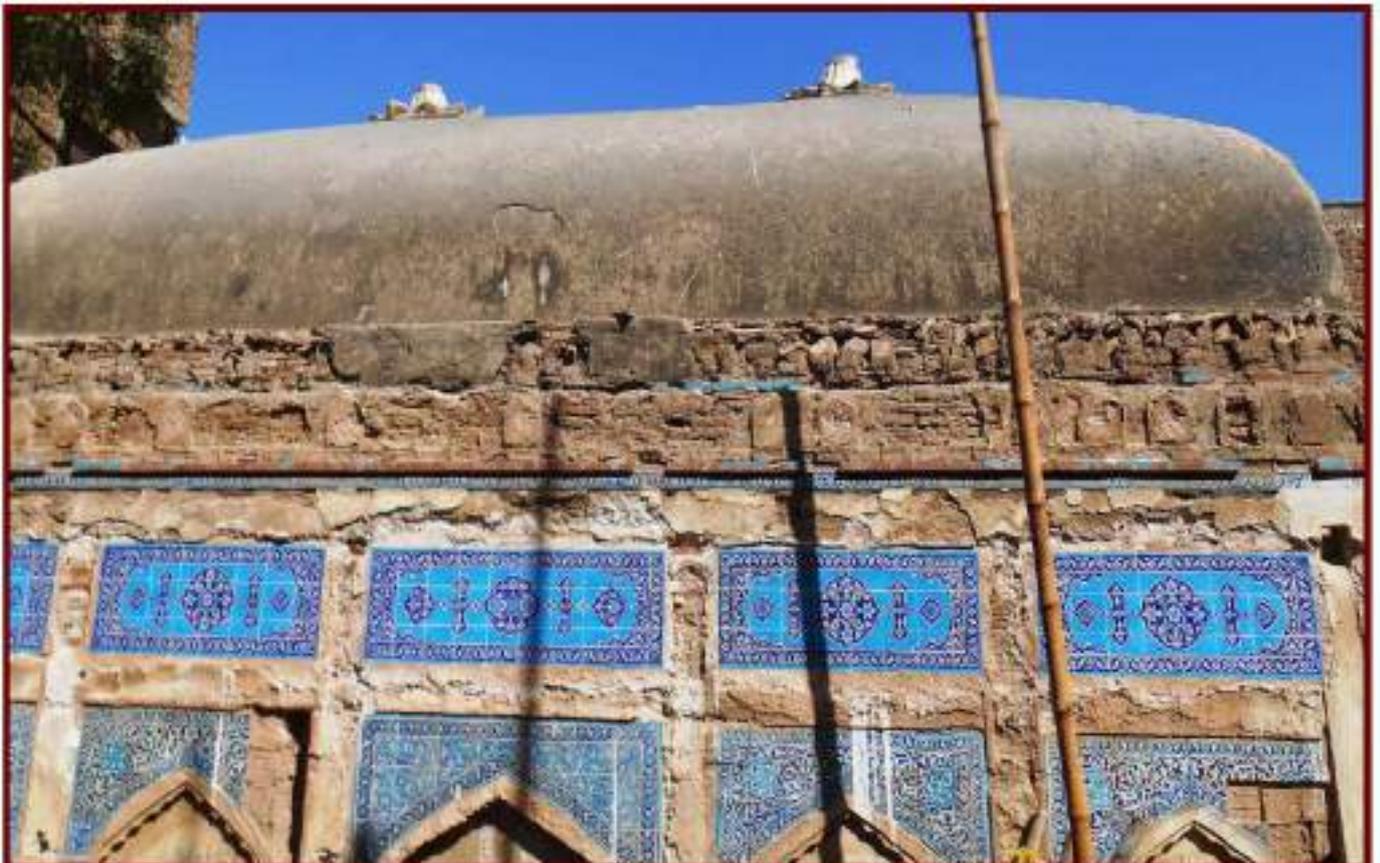

Facade of Tajjar M-6

Mir Karam Ali Khan Talpur Tombs (Complex)

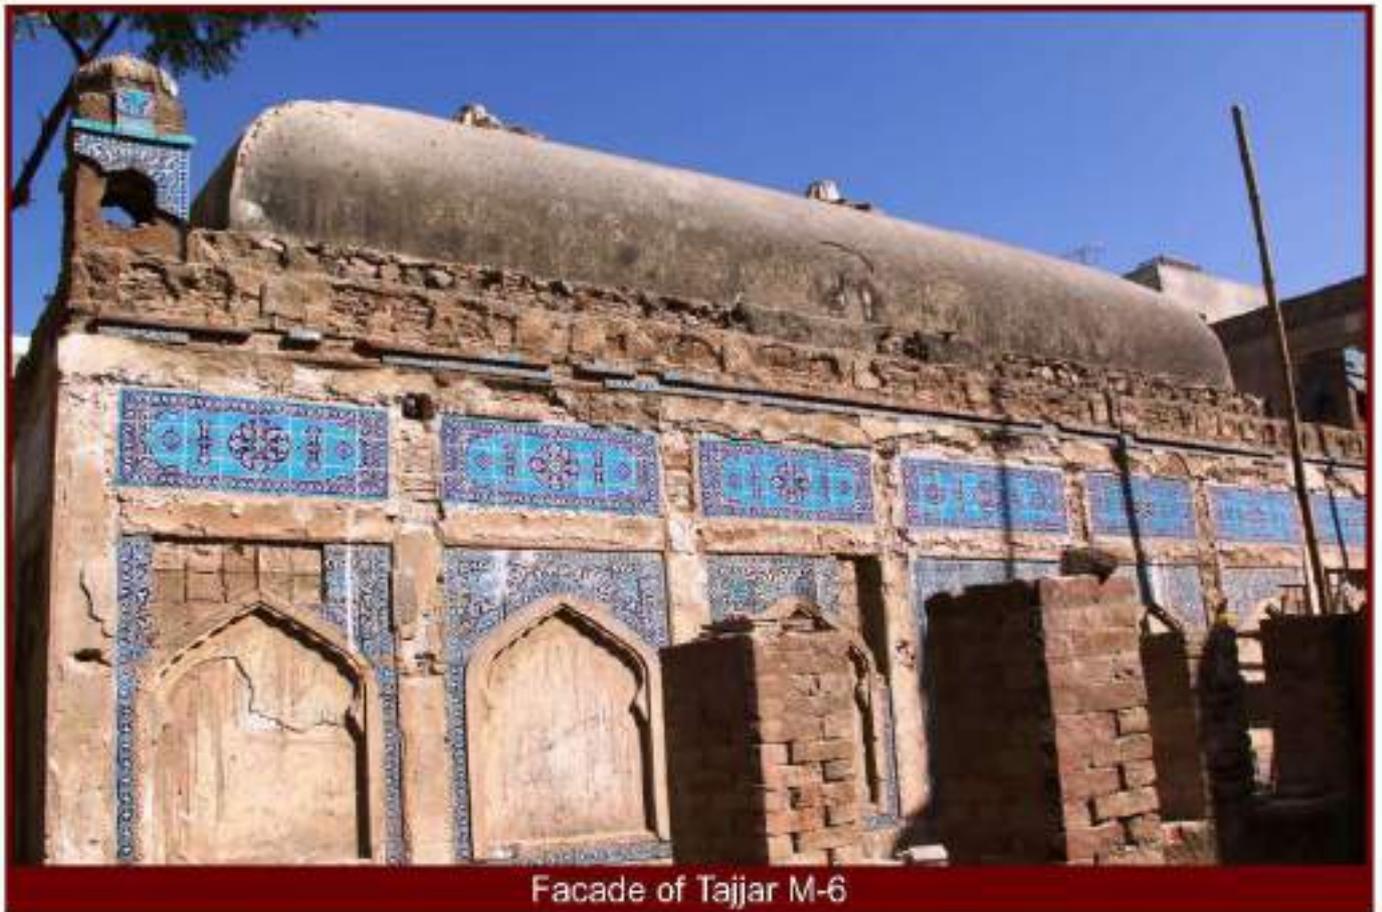


Facade of Tajjar M-6



Northern side of Tajjar M-3

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex

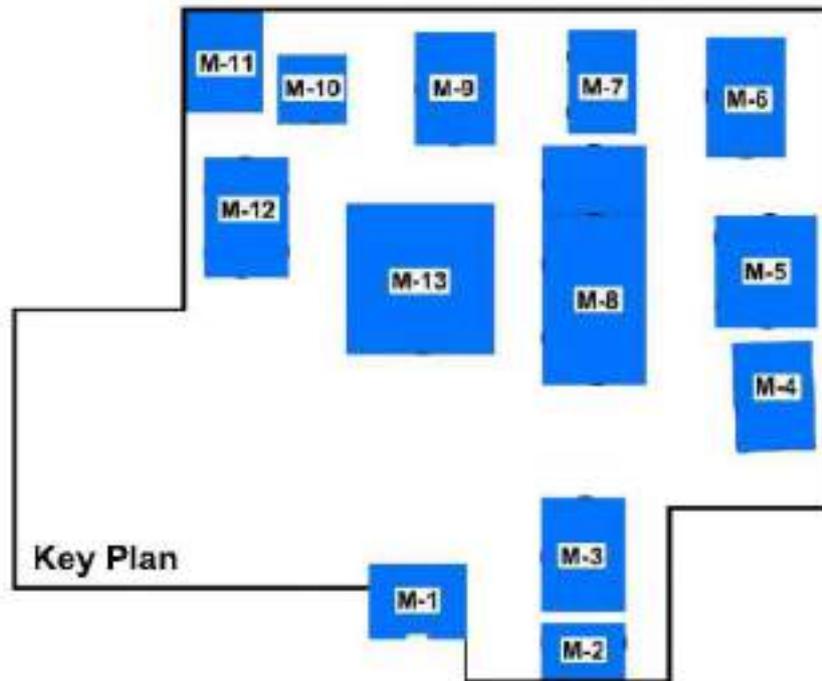

M-13 | Mir Karam Ali Khan Talpur Tomb

- After scraping the top of dome. It is coated with two layers of chiroli and two layers of lime. Then lime cream and soapstone is used.
- Finial are fixed on the top of the dome.
- Turrets of Mir Karam Ali Khan Talpur are finally restored and finial are fixed.
- Facade of Mir Karam Ali Tomb is Exclusively Redecorated.
- Southern side of Tomb is entirely conserved.
- Western side of Tomb plastered and tiles are fixed.
- Northern Side of Mir Karam Ali Khan Talpur Tomb is restored and tiles are refixed.
- Fresco work on the inner wall of the tomb is in momentum.

M-1 | Entrance Gate

- Eastern and Western side of Main Entrance are preserved.
- The northern side is totally plastered.
- Fresco work on the inner dome of main entrances is in advancement.

M-8 | Flat Roof Structure (Mir Naseer Khan Talpur's Tomb)

The cracks and wholes in roof are filled.
 The façade of Southern side of Mir Naseer Khan Talpur is protected.
 Eastern side is entirely refurbished.
 The Northern side of Tomb is exclusively preserved.
 Western side of Mir Naseer is restored.
 Finial are fixed on the restored turrets of Mir Naseer Khan Talpur's Tomb.

M-4 | Vaulted Roof Structure

Lime Plaster at the top of vaulted roof is completed.
 Finial at the top of vaulted roof are restored.
 Corner Turrets are restored on the facade of M4.
 Kashi Work of Tajjar M-4 on the Northern Side of Mir Naseer Khan Talpur is completed.
 Tiles are fixed on facade and also lime work is completed.

Mir Karam Ali Khan Tombs Complex

M-3 | Vaulted Roof Structure

- Lime plaster at the top of vaulted roof is completed.
- The facade of M3 are fully restored.
- West side of "Tajjar" is completed.
- North and East sides are exclusively completed.
- M-2 | Flat Roof Small Structure
- Northern side is finalized.
- Western side is restored.
- Southern side plastered with Chirolu & lime.

M-6 | Tajjar

- Kashi tiles on the top of horizontal panels of northern side of M-6 is fixed.
- Facade of M-6 is restored with Kashi and plastered with chirolu and lime.
- Eastern side is fully restored.
- Northern side kashi and plastered work is in progress.

M-9

- Eastern side of M-9 is preserved.
- Southern wall is restored.
- Northern wall of Tajjar are protected.
- Work is in progress on western wall.

M-5 | Flat roof structure

- Facade of flat roof structure is totally conserved.
- Western wall of M-5 plastered and kashi are fixed.
- Eastern side is also refurbished only one panel is under progress.
- Three turrets are preserved only one remained.

Flooring


- Brick flooring is 95% is renewed.

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Western side of Main Entrance is completely restored

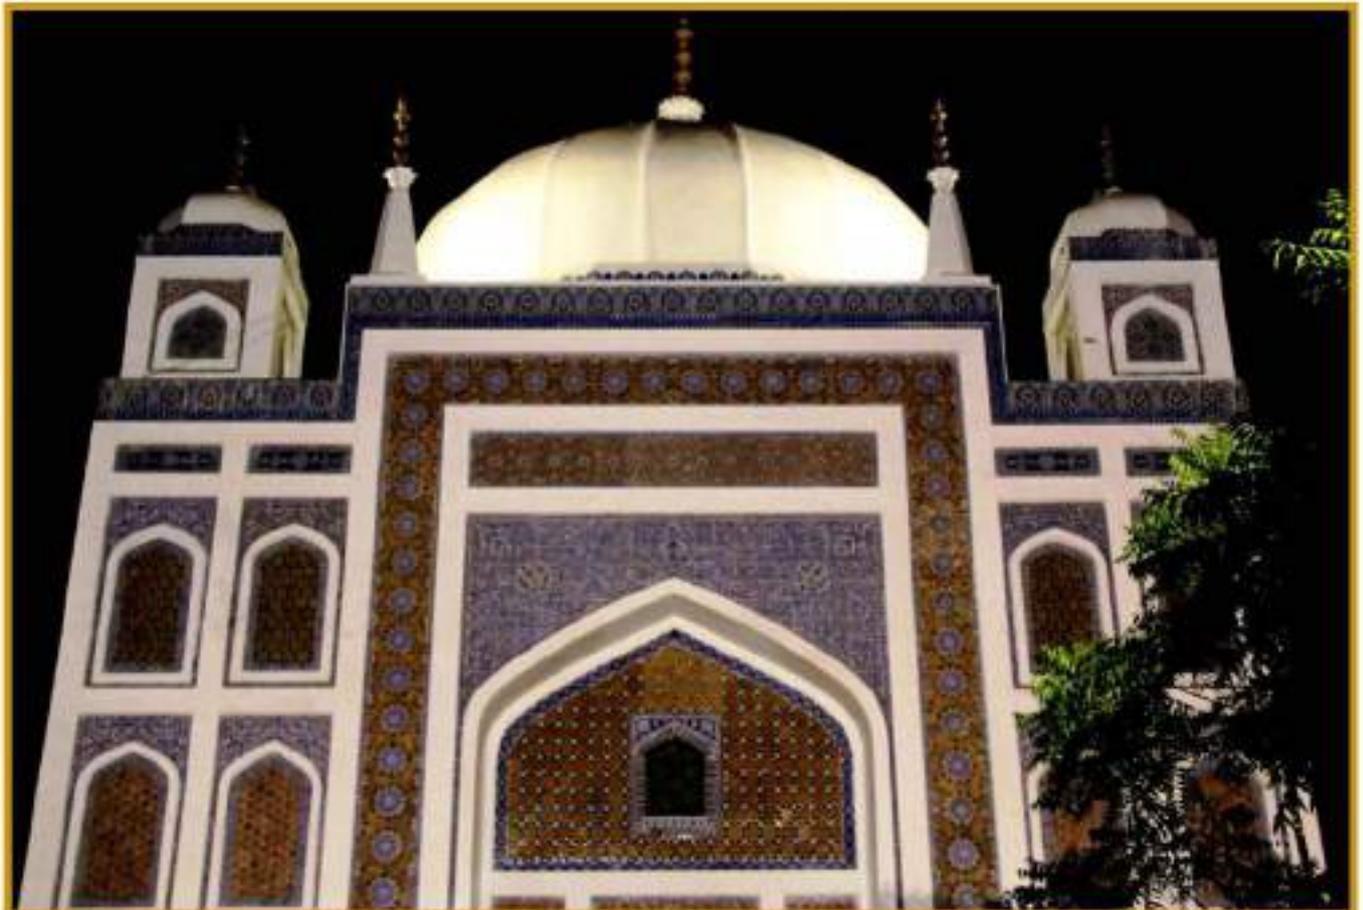

Spotlighted facade of Mir Karam Ali Khan tomb

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Dome of Main Entrance & Mir Karam Ali Tomb After Restoration

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Brick Flooring



Brick Flooring at Night Shift

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Restored facade & eastern side of Mir Naseer Tomb



Tajjar M-4 After Restoration

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex




Western side of M-3 after conservation



Restored Walls of M-6

Mir Karam Ali Khan Tombs Complex

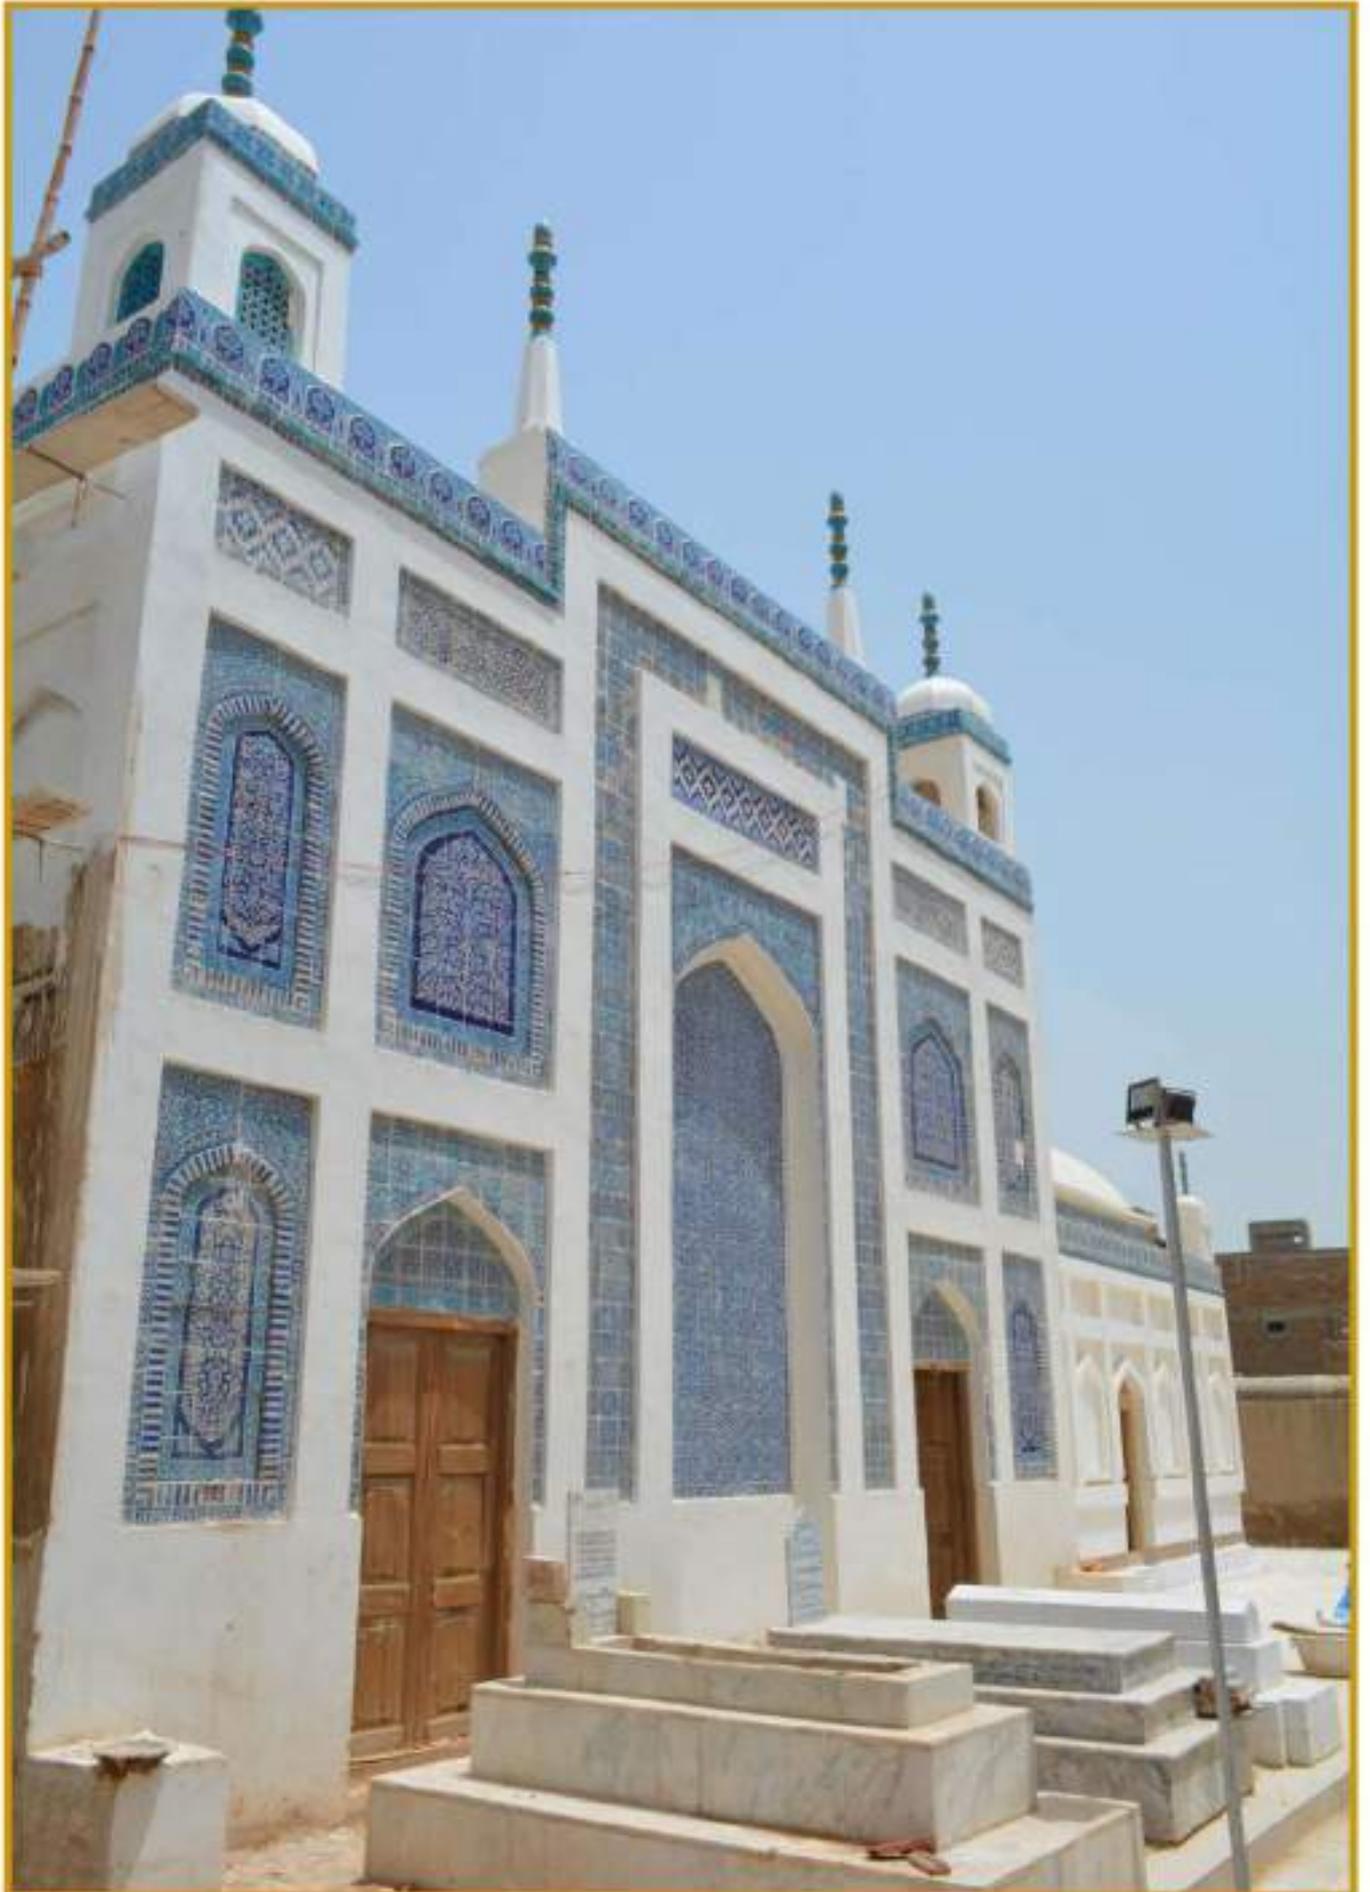

Redecorated Elevation of Mir Naseer Tomb

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Tajjar M-9 After Restoration



Fresco at inner side of main entrance gate

Mir Karam Ali Khan Tombs Complex



M-13 | Mir Karam Ali Khan Talpur's Tomb

- ✓ External Structure of Mir Karam Ali Khan Tomb is Exclusively Restored with two layers of Chiroli, two layers of lime, lime Cream paste and Soapstone.
- ✓ New Finial is fixed on the top of the dome and Turrets are completely restored and fixed.
- ✓ Kashi Tiles of Mir Karam Ali Tomb is Exclusively Restored and Replaced.

Mir Karam Ali Khan Tombs Complex

M-1 | Entrance Gate

- ✓ Main entrance gate is completely resorted with similar materials.
- ✓ Main entrance wooden door is fixed.
- ✓ Fresco work on the inner dome of main entrances is in advancement.

M-8 | Flat Roof Structure (Mir Naseer Khan Talpur's Tomb)

- ✓ The cracks and holes of the roof of Mir Naseer Khan Talpur's are repaired and conserved with lime plaster.
- ✓ Exterior walls of entire structure are Exclusive repaired with two layers of Chiroli, two layers of lime, lime cream paste and soap stone.
- ✓ New Finial is fixed on the Mir Naseer Khan Talpur's Tomb.

M-4 | Vaulted Roof Structure

- ✓ The top of vaulted roof is completely restored with Lime Plaster.
- ✓ Finial and Turret at the top of vaulted roof is restored.
- ✓ Exterior Walls are completely restored with two layers of Lime Plaster.
- ✓ Kashi Tile Work of Tajjar M-4(Mir Naseer Khan Talpur's) is completed.

M-3 | Vaulted Roof Structure

- ✓ The top of vaulted roof is completely restored with Lime Plaster.
- ✓ Exterior walls of Entire structure are Exclusive Restored with Chiroli and Lime Plaster.
- ✓ M-2 | Flat Roof Small Structure
- ✓ Entire Structure of M-2 Flat Roof Structure is completely restored with Chiroli and Lime Plaster.

M-6 | Tajjar

- ✓ Tajjar Structure is Exclusively Restored with two layers of Chiroli, Lime Plaster.
- ✓ Kashi tile work is exclusively completely from external walls.

M-9

- ✓ M-9 structure is completely restored and preserved with Chiroli and Lime Plaster.

M-5 | Flat roof structure

- ✓ Flat roof structure is completely restored and conserved with Chiroli and lime plaster.
- ✓ Kashi tile work is exclusively completely on external walls.
- ✓ Four numbers of turrets are completely restored and preserved.

Flooring

- ✓ Brick flooring is completed in Entire Complex.

Electrification Work

- ✓ Lighting work in entire Mir complex is completed.


CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Restored colourful panel at Mir Karam Ali Khan Talpur's Tomb

Mir Karam Ali Khan Tombs Complex

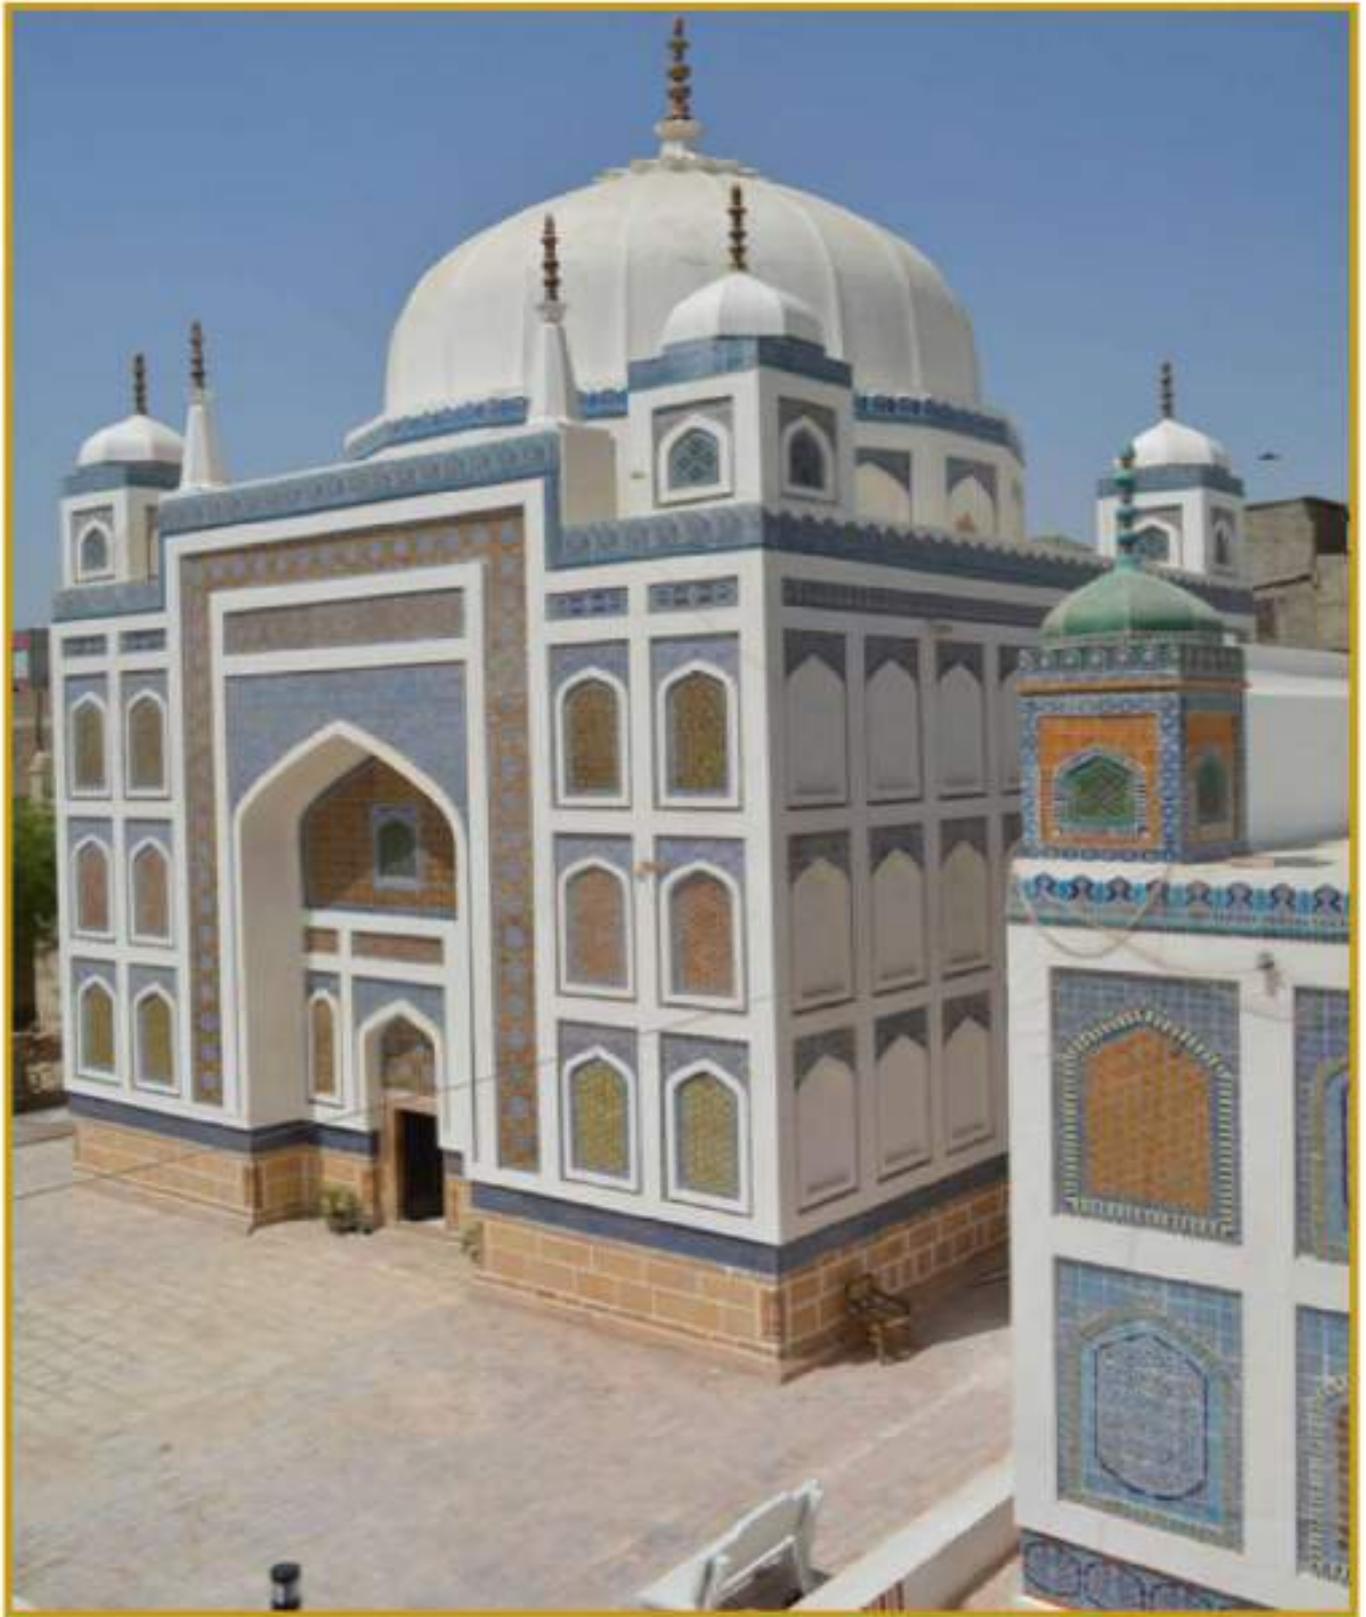

Mir Karam Ali Khan Talpur's Tomb after restoration

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Restored Tajjar



Main Entrance

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Restored floral design inside inner walls of main entrance M-1


CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Brick pavement at Mir Karam Ali Khan Talpur's Tomb Complex

Mir Karam Ali Khan Tombs Complex

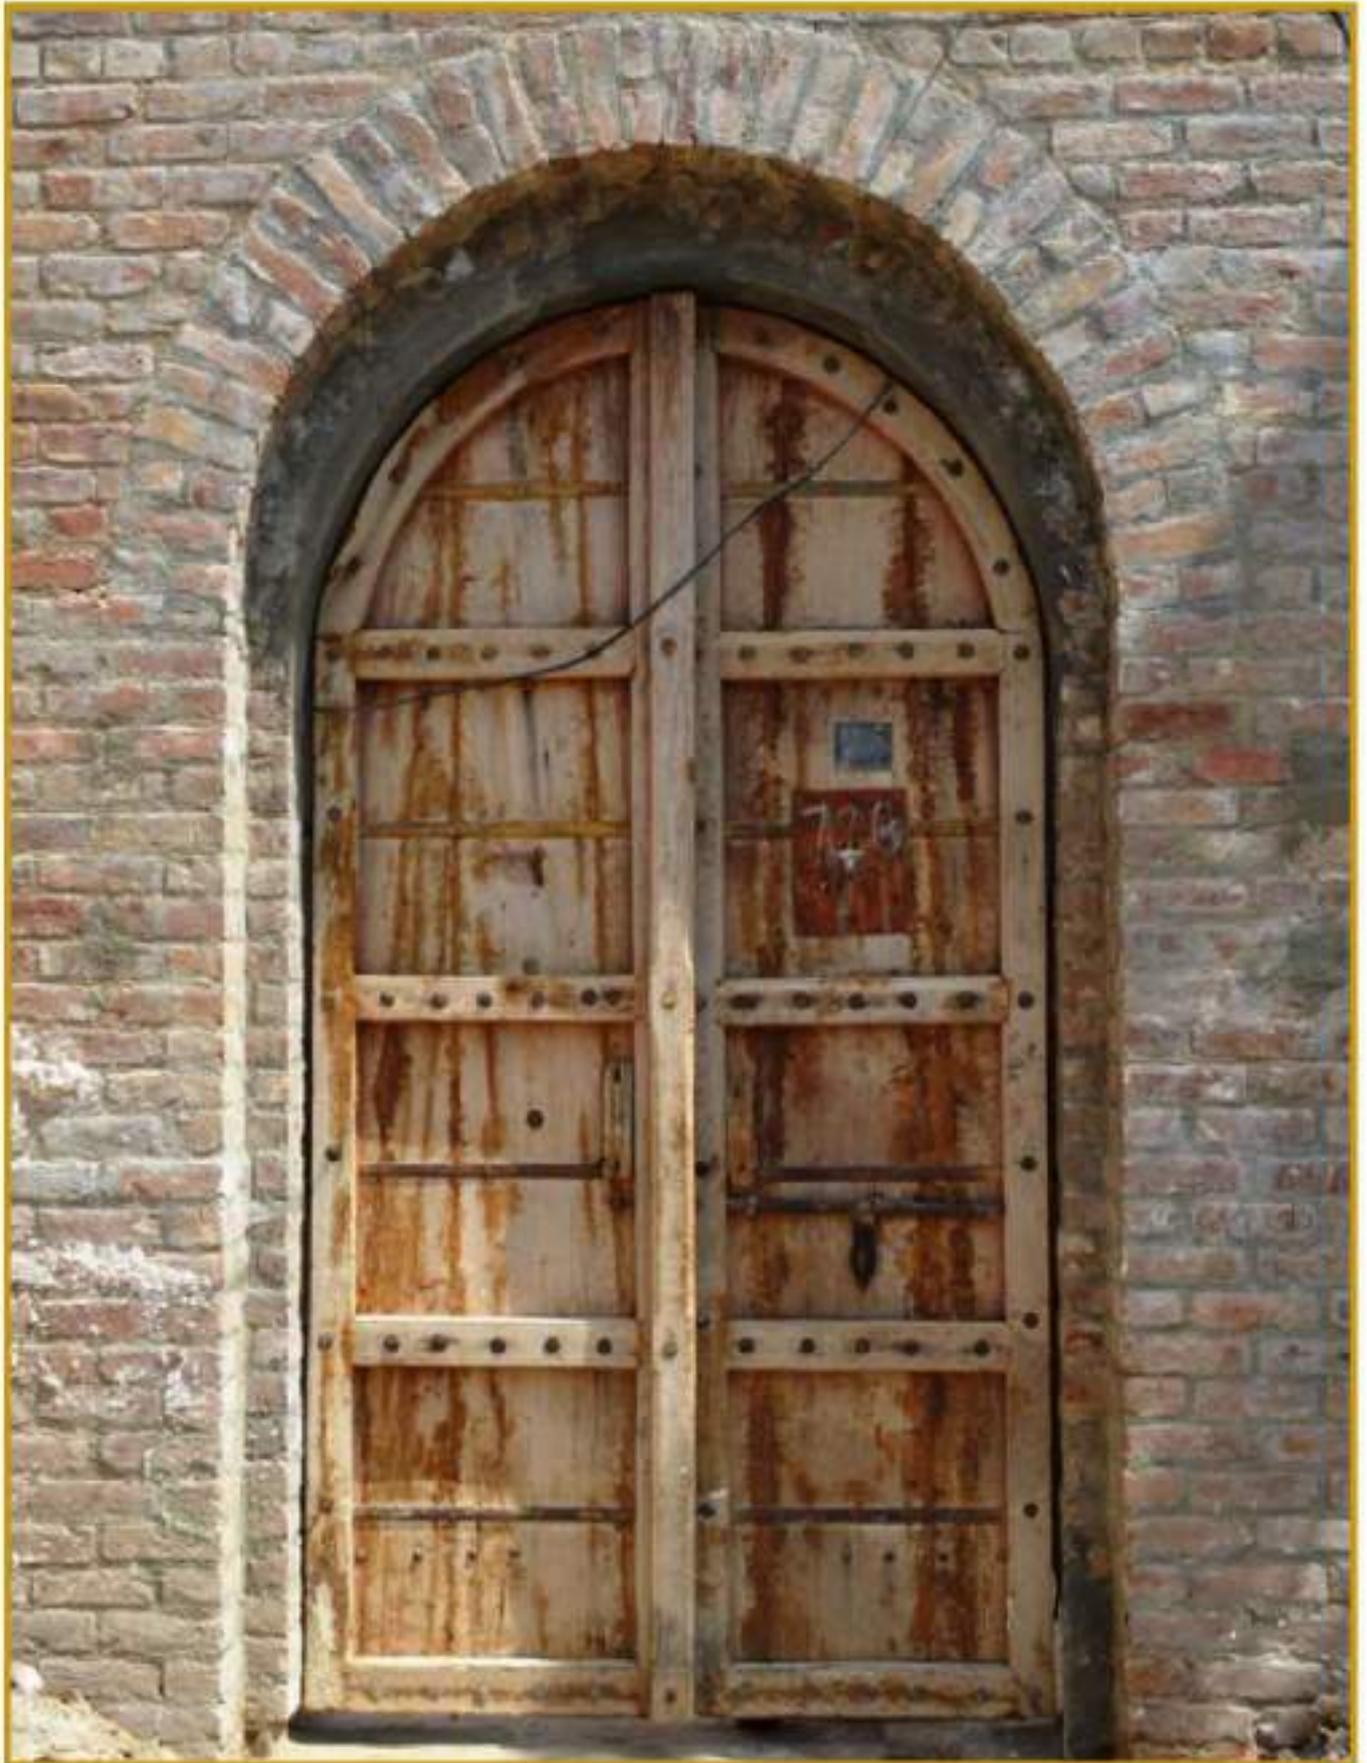

Wooden door is fixed at Mir Karam Ali Khan Talpur's Tomb Complex

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



New wooden carved door is fixed at main entrance gate M-1

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Brick pavement is completed between main entrance and the steps of Mir Karam Ali Khan Talpur's Tomb

CONSERVATION PROGRESS

Mir Karam Ali Khan Tombs Complex



Mir Karam Ali Khan Talpur's Tomb Complex after restoration

Mir Karam Ali Khan Tombs Complex

M-13 | Mir Karam Ali Khan Talpur Tomb

à Hexagonal (Chaaka) tiles of bottom arches on the facade of tomb is replaced.

M-1 | Entrance Gate

(Completely Restored)

M-3 | Vaulted Roof Structure

(Completely Restored)

M-4 | Vaulted Roof Structure

(Completely Restored)

M-5 | Flat roof structure

(Completely Restored)

M-6 | Tajjar

(Completely Restored)

M-8 | Flat Roof Structure (Mir Naseer Khan Talpur`s Tomb)

(Completely Restored)

M-9

(Completely Restored)

Flooring

(Completely Restored)

Electrification Work

à Lighting work in entire Mir complex is completed.

Mir Karam Ali Khan Tombs Complex



Replaced Hexagonal (Chaaka) tiles on the bottom right arch of facade of Mir Karam Ali Talpur Tomb



Replaced Hexagonal (Chaaka) tiles on the bottom left arch of facade of Mir Karam Ali Talpur Tomb
